


METHOD STATEMENT

09-07-2024

WORK ACTIVITY:	Mechanical demolition Ridley Wood
METHOD STATEMENT NO:	FI CON Ridley wood
PROJECT:	Ridley Wood
SITE ADDRESS:	Units 1-9 Ridley Wood Industrial Complex
CLIENT:	FI Real estate Management Ltd
CLIENT REPRESENTATIVE:	Boris Byrne
RAMS REQUESTED BY:	John Lohan
RAMS PRODUCED BY:	George Steele
RAMS IN ACORDANCE WITH:	BS6187:2011 Code of practice for full and partial demolition.
HEALTH & SAFETY MANAGER:	Project four Safety consultancy

INTRODUCTION:

The purpose of the demolition method statement is to outline our approach to managing the demolition works for the mechanical demolition at Ridley Wood. This document Includes specific comments on the site establishment, logistics, and the process of managing the overall environment and surrounding property. It will also ensure that the demolition and associated works cause the minimum disruption to the adjacent businesses with a safe working and living environment maintained. The agreed contents of the demolition method statement will form part of the development plan and will be agreed with FI Construction Ltd site team. The plan will be constantly reviewed, and any changes or improvements will be added and agreed, the plan will then be revised and re- issued.

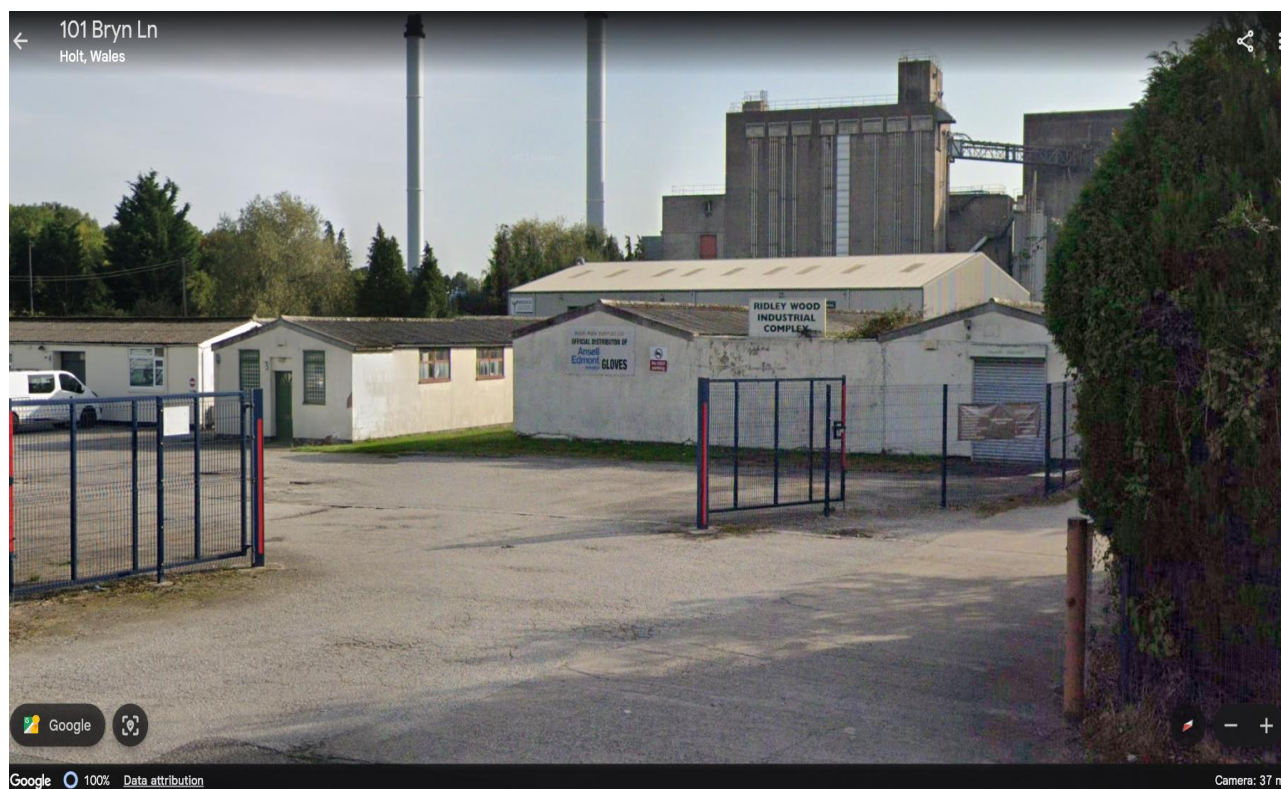

BRIEF DESCRIPTION OF WORKS TO BE UNDERTAKEN

DESCRIPTION OF WORKS:	To mechanically demolish multiple units using a series of demolition excavators fitted with rotating pulverisers and demolition sorting grabs.
------------------------------	--

TRAINING FOR OPERATIVES ON SITE
INDUCTION TRAINING
Prior to any operatives commencing works on site they will receive health and safety induction training by the demolition site manager or supervisor FI Construction Ltd
RISK MANAGEMENT, DABS, DAILY ACTION BRIEFING
All operatives associated with site activities which create significant risk of injury will be specifically briefed in the hazards and control measures applicable to the safe system of works. All operatives receiving daily briefings will sign documentation to say they fully understand the risks and control measures implemented to ensure the safety and wellbeing of themselves and others.
SPECIFIC TRAINING
All operatives / operators / managers / or supervisors must hold the appropriate training cards or certificate of training achievement relevant to their positions on site.
TOOL BOX TALK TRAINING
Toolbox talk training will be used to instruct and train employees on specific site tasks, as and when necessary. The manager, supervisor or designated operative presenting the toolbox talk must try to promote an open discussion with all the site team. The presenter must discuss the risk elements of the tasks being discussed and try to get feedback from the site team on the best way of controlling the risks. Feedback from the workforce and actions implemented via the toolbox talks will ensure that everyone feels included and that their participation is meaningful. All toolbox talks and actions because of the toolbox talk must be recorded and signed by all attendees; the record must then be entered into the site file.

TRAINING & PERSONNEL		
PROJECTS MANAGER  FI CONSTRUCTION & DEMOLITION	Daniel Burrows	CCDO GOLD CARD DEMOLITION SUPERVISOR CPCS EXCAVATOR OPERATOR FIRST AID AT WORK CPCS EXCAVATOR OPERATOR MEWP OPERATOR NNLW ASBESTOS REMOVAL COURSE
SITE MANAGER  FI CONSTRUCTION & DEMOLITION	Martin Shone	CCDO GOLD CARD DEMOLITION SUPERVISOR CPCS EXCAVATOR OPERATOR SLINGER SIGNALLER FIRST AID AT WORK BOBCAT SKID LOADER NNLW ASBESTOS REMOVAL COURSE
SITE SUPERVISOR  FI CONSTRUCTION & DEMOLITION		CCDO DEMOLITION OPERATIVE CPCS EXCAVATOR
SITE OPERATIVE  FI CONSTRUCTION & DEMOLITION		CCDO DEMOLITION OPERATIVE NNLW ASBESTOS REMOVAL COURSE CPCS EXCAVATOR
SITE OPERATIVE  FI CONSTRUCTION & DEMOLITION		CCDO DEMOLITION OPERATIVE NNLW ASBESTOS REMOVAL COURSE CPCS EXCAVATOR
SITE OPERATIVE  FI CONSTRUCTION & DEMOLITION		CCDO DEMOLITION OPERATIVE NNLW ASBESTOS REMOVAL COURSE CPCS EXCAVATOR

PLANT & EQUIPMENT	
PLANT:	Multipul Demolition specification 360' excavators
ATTACHMENTS:	360- degree rotating combination shear (capable of cutting steel and concrete) 360- degree rotating demolition grab Test certificates for the equipment as required under PUWER will be supplied upon delivery to site and prior to any works commencing. NOTE – the excavators are demolition plant and are not classed as lifting devices when carrying demolition attachments and do not come under LOLER when operating as demolition excavators. Mobile crusher
WORK EQUIPMENT:	Dust boss / dust management unit High powered jet wash Hose pipe for dust suppression Heras's fencing panels

PPE	
MANDATORY PPE:	Hard hat (BSN397) Safety boots (BSN345 steel toe cap & steel midsole) Hi visibility vest or jacket (class 2) Safety Spectacles (1F) Gloves (KV2101)
TASK SPECIFIC:	RPE with P3 filters (all operatives face fitted, cleanly shaven every day)

PUBLIC INTERFACE ARRANGEMENTS	
SEGREGATION: PROTECTION:	Temporary exclusion zones will be erected during specific stages of the demolition. The details of the exclusion zones are attached. The pavements will be cleared at the end of each working day along care will be taken to ensure that emergency vehicle access is not impeded.

DRAWINGS / SURVEYS	
SURVEYS:	A photographic dilapidation survey of the pavement and road will be undertaken prior to commencing demolition activities and forwarded to head office for information. N/A
DRAWINGS:	
PERMITS:	Permit to excavate to be issued prior to any excavations

ENVIRONMENTAL / MONITORING	
DUST:	Monitoring Site Impacts Dust Dust is often the most notable nuisance when it comes to negative demolition impacts. Unlike noise and vibration dust remains long after the operation that caused it has ceased. In addition to its unsightliness dust can be damaging to health as well as detrimental to property. Given the central location of the project it will be necessary to adopt robust procedures for dealing with this issue. Dry spells during the summer months are the most likely times of year where dust can become a nuisance not least because of the lack of moisture to dampen down particles stopping them from becoming airborne. This will, therefore, require a monitoring and management regime to be employed by site staff. Measures to reduce dust during the demolition works will include the following: • High specification dust Suppression equipment [DUST BOSS] will be used to dampen down dust in all working areas. • A high- powered Jet wash unit will also be on standby as a backup dust suppression unit. • Rigorous Housekeeping and general cleanliness on site. • Use of road sweepers vacuums where practicable.

SERVICE DISCONNECTIONS / ISOLATIONS	
Electricity	➤ Isolated ➤ Disconnected

Sign off.....Comments

SERVICE DISCONNECTIONS / ISOLATIONS	
Gas	➤ Isolated..... ➤ Disconnected.....

Sign off.....Comments

SERVICE DISCONNECTIONS / ISOLATIONS	
Water	➤ Isolated

Sign off.....Comments

ASBESTOS SURVEY / REMOVAL	
Asbestos	

Sign off.....Comments

ENVIRONMENTAL SURVEY	
	See site file

ECOLOGY	
	See site file

TREE PROTECTION	

SEQUENCE OF TASKS

The Site Supervisor/Manager will ensure this method statement and risk assessment is explained and briefed to all operatives involved in the task. All operatives will sign to confirm they have understood this method, the risks involved and the control measures put in place.

Activity 1 – Erect exclusion zone



- A1.1 An exclusion zone will be erected as shown picture below. This area will be controlled by FI Construction Ltd banksman during the demolition operations. The banksman will be in contact with the excavator operator and the FI Construction and Demolition Ltd site manager.
- A1.2 The exclusion zone will be controlled by a minimum of two operatives always acting as banksman. The banksman will be always in visual contact with the excavator operator and Site Manager. The banksman will have full authority to stop works at any time during the demolition operations. If at any time access is required by emergency vehicles or delivery driver's demolition works will cease and the exclusion zone gates will be opened to allow controlled access past the demolition works.
- A1.3 The demolition works will be carried out within the exclusion zone. Banksman will control vehicle in and out of site. No reversing outside site without a banksman.



Activity 2 - Set up dust suppression

- A2.1 Water suppression will be set up to enable a constant spray of water to be directed onto the structure during mechanical demolition. The water suppression is a direct feed water system that enables a fine mist to be sprayed close to the end of the pulveriser that is fitted to the excavator.



Activity 3 - Commence mechanical demolition

- A3.1 A 360 Excavator fitted with a rotating demolition sorting grab will commence to demolish the first section of the single storey building. The operator will strip off the roof trusses and will place them directly into a 45 yard bin
- A3.2 The operator using the 360 excavator fitted with the sorting grab will then reduce the walls down to slab level. The demolition arisings will be separated for recycling as described in activity 4.
- A3.3 Once the walls are down and removed the excavator operator using the 360 excavator fitted with a bucket will commence lifting the slabs and foundations. The slabs will be lifted and processed using a concrete pulveriser. The demolition arisings will be separated and stockpiled for crushing.

Activity 4 – Segregation and recycling

- A4.1 The site team using multiple excavators fitted with sorting grabs, demolition shears and pulverisers will commence sorting through the demolition arisings.
- A4.2 The excavator operators will sort through the demolition arisings and place the separated products into pile for recycling. The teams will have skips and bulker trailers at hand to load away all recyclable materials.
- A4.3 The excavator operators will spread demolition arisings into a safe area where operatives can sort through without risk of being struck by excavators or moving vehicles. Operatives working in the safe area will sort through the debris pulling out any cable or non-ferrous metals for recycling. The recycling materials will be placed into 10- yard bins to be sent to the recycling facility.
- A4.4 At this point the site will employ three excavators fitted with processing equipment to pulverise all the demolition arisings ready to be placed through the crushing plant. The crushing plant will separate all materials and will produce a 6F2 product for recycling. The crushing plant will have two sources of dust suppression, the first will be a direct water feed onto the crushing belt to dampen the crushed materials art source. The second will be the continued use of the Dust Boss, to be used on a self-rotating mode that can be adjusted to suit weather conditions ie, wind and dry conditions.

Section 2

MECHANICAL DEMOLITION RISK ASSESSMENTS

What are the hazards	Who might be harmed and how	Risk rating before control measures have been implemented	What control measures are in place	Risk rating after control measures have been implemented
Manual Handling	Operatives may suffer broken bones, cuts or lacerations from handling materials.	Medium	Operatives to wear gloves, hard hats, safety spectacles and steel toe capped boots with steel midsoles	Low
	Operatives may suffer muscular skeletal injuries when manually handling materials.	High	360 excavators to be utilised to demolish the building and move loads where possible. - If manual handling has to be carried out assess the loads before lifting, if required break down the load into manageable weights & sizes using handheld tools - Kinetic lifting techniques to be used to lift all loads. - All operatives to have undergone manual handling training.	Low
Slips & trips	Operatives & members of the public may suffer broken bones, sprains or cuts due to tripping over materials	Medium	- Pedestrian access routes to be kept clear of all materials. - Pedestrian routes to be clearly lit. - Exclusion zones to be banked and manned. - Exclusion zones to be removed at the end of each working day.	Low
Falling objects	Operatives on site and members of the public may suffer serious or minor injury due to falling materials	High	- Site to be enclosed with fencing prior to commencing demolition. - No operatives are to be inside the building during mechanical demolition. - Operatives to wear hard hats and steel toe capped & steel mid sole safety boots. - No loads to pass over the top of any operatives. - Banksman to be used on site to ensure no personnel encroach into the demolition area. - Excavator operator to be experienced in demolition works. - Building to be demolished in bays ensuring the building is never undermined. - Building to be left in a safe state at the end of each shift.	Low

			- Sequence and methodology to be approved by a structural engineer. - Arisings to be scrapped off the floors to prevent overloading. - Road narrows and road closures to be implemented during certain phases of the demolition process.	
Excavator operations	Operatives on site & public may suffer fatal or serious injury if struck by an excavator	High	- Plant operators to be trained and competent. - Always approach excavator from the front & ensure operator has contacted you prior to walking into the arc of the excavator. - Never walk into the arc of the excavator - Ensure site traffic management plan is followed on site. - Exclusion zones to be erected around the site.	Low
	Excavator operator may suffer fatal or serious injury due to excavator overturning	High	- Excavator operator to wear seat belts at all times. - Excavator to be operated on firm level ground.	Low
	Site operatives may suffer fatal or serious injury due to incorrect use of quick hitch, working under attachments or if the attachment becomes detached from excavator Excavator operators may suffer serious injury when re-fuelling excavators.	High	- All plant operators to have undergone quick hitch training. - All plant operators to use quick hitch as per manufactures instructions. - Attachments or loads must not be manoeuvred over the top of any personnel and must not be slewed over any of the site boundary - Excavator operators must be extremely careful when re-fuelling excavators. - Operators must use safe platform when re-fuelling. - Operators must be careful not to spill fuel when filling up. - Mobile towers may have to be introduced when filling up if excavators are not fitted with a boxing ring. - Operatives must carry out a risk assessment prior to filling up excavators.	Low
Contact/strikes of live utility services	Plant operator operatives may suffer fatal or serious injury if electric cables or gas pipes are struck	High	- All utility services to be disconnected prior to commencing mechanical demolition. - Utility disconnection paperwork to be located within the CPHSP	Low
Contact / being struck by HGV's	Operatives on site may suffer fatal or serious injury if struck by an HGV	High	- Ensure site traffic management plan is followed on site. - Any reversing into site must directed with the aid of a banksman.	Low
Dust during demolition activities	Operatives and members of the public may suffer minor respiratory problems due to dust being created from	High	A minimum of two dust units to be used on this project, including a specialist dust boss unit.	Low

	mechanical demolition activities		Water will be directed onto the building to suppress any dust that may occur from demolition activities	
Noise during demolition activities	Members of the public and may suffer nuisance noise during mechanical demolition	High	Structure to be demolished using a pulveriser to reduce the noise	Low
Collapse of building	Members of the public and may suffer fatal injuries if building collapses during mechanical demolition.	High	- Structure to be demolished working in bays ensuring that the building is stepped, and the floors are cleared of demolition arisings as the demolition progresses through the structure. - Exclusion zones to be implemented around the structure. - Road narrows and road closures to be implemented during certain phases of the demolition process.	Low

Section 3

**I confirm I have read and understood the method statement and risks involved
and will work in accordance with the method statement as described**

OPERATIVE SIGNATURES			
Name	Signature	Date	Revision No.

AMENDMENTS		
Time/Date	Description of amendment	Signature of Manager/Supervisor

Method Statement Produced By: George Steele	09-July- 2024
Method Statement Approved By: John Lohan	
