

BS 5837:2012

Method Statement

13th October 2023

Report No. LTM0907.MS.02

Project: Land adjacent to Smithy View
Garage

Authored by: Matthew Lally



METHOD STATEMENT

PROJECT

Land adjacent to Smithy View Garage

Chester Road

Wrexham

LL12 8DY

LALLY TREE MANAGEMENT

36 Goldsworthy Road,
Urmston,
Manchester,
M41 8US
[T] 07305 740120

[E] matt@lallytreemanagement.co.uk
[W] <https://www.lallytreemanagement.co.uk/>

DOCUMENT ISSUE RECORD

Date of Inspection	Surveyor	Report Version	Issue Date	Author
15.09.2023	Matthew Lally. FdSc MArborA	02	13.10.2023	Matthew Lally. FdSc MArborA

This report is the property of Lally Tree Management. This report may only be reproduced or disclosed to third parties with express written consent from Lally Tree Management.

All comments, conclusions and recommendations within this report are based on the information available to Lally Tree Management at the time of investigation. Lally Tree Management accepts no liability in cases where provided information is found to be inaccurate or misleading or if additional information exists or becomes available.

CONTENTS

1. INTRODUCTION	1
1.1. Author Information & Report Purpose	1
2. GENERAL INFORMATION	1
2.1. Understanding Tree Roots and Damaging Factors.....	1
3. METHOD STATEMENT	2
3.1. Sequence of Events.....	2
3.2. Pre-commencement Site Meeting.....	2
3.3. Tree Works.....	3
3.4. Site Briefing	3
3.5. Protective Fencing	4
3.6. Additional Precautions Outside Fenced Areas	6
3.7. Cellular Confinement System.....	6

Appendix I Tree Removal Plan & Tree Protection Plan

1. INTRODUCTION

1.1. Author Information & Report Purpose

- 1.1.1. My Name is Matthew Lally (FdSc) and I have created this Method statement to outline the required steps which must be implemented to successfully retain the trees we wish to retain without adversely affecting their safe useful life expectancy. The steps in this Method Statement must be followed and if there is any misunderstanding or difficulty with these steps then I must be contacted immediately to clarify any issues.
- 1.1.2. Failure to adhere to the recommendations outlined in this document could result in tree decline or tree death which will mean a breach of planning consent. The trees outlined for retention in this document are protected by planning law and any tree loss and damage could result in prosecution.

2. GENERAL INFORMATION

2.1. Understanding Tree Roots and Damaging Factors

- 2.1.1. It is important to understand that the majority of the root system is within the top 600mm of the soil extending radially for distances in excess of the Root Protection Area (the Root protection Area is simply the minimal amount of untouched root system deemed to be required for this tree to be successfully retained). Beyond the main structural roots (close to the base of the trunk), the root system rapidly sub-divides into smaller diameter roots: off this main system, a mass of fine roots develops which are incredibly important for the tree to be able to take up water and essential nutrients.
- 2.1.2. These very fine roots are easily damaged by a number of factors such as: -
- a) Compaction of the ground, which reduces the space between soil particles. This is particularly important on clay soils. A single passage by heavy equipment on clay soils or storage of heavy materials can cause significant damage.
 - b) Changing soil levels, even for a few weeks.
 - c) Covering the root area with impervious surfaces.
 - d) A rise in the level of the water table. Roots can tolerate submersion for short periods. But a permanent rise will deplete the soil of oxygen.
 - e) Stripping the topsoil, such works must be avoided until protective fencing has been erected.
 - f) Pollution, such as cement washings & oils.

- g) Excavations in the root protection area. Even shallow excavations can cause damage and therefore must be avoided unless otherwise stated in this document.

3. METHOD STATEMENT

3.1. Sequence of Events

- 3.1.1. I have compiled the sequence of events below that must be undertaken in the order stated. Each step listed below is then expanded upon in 3.2 onwards to ensure the requirements for each step are understood. This sequence should be read in conjunction with the Tree Protection plan in appendix I.

- 1) Pre-commencement site meeting (See 3.2)
- 2) Tree removal and tree pruning (See 3.3)
- 3) Site briefing for personnel (See 3.4)
- 4) Installation of protective fencing (See 3.5)
- 5) Implementation of development (See 3.6 & 3.7)
- 6) Completion of development works
- 7) Removal of protective fencing
- 8) Completion signed off

3.2. Pre-commencement Site Meeting

- 3.2.1. Prior to commencement of any site works or tree works, a meeting must take place including the Site Manager and an Arboricultural Consultant. This meeting can be onsite, virtual or over the phone and will allow further discussion of the programme of works, tree protective measures, locations of areas for storage/site organisation and the agreement of any changes to the Method Statement that may be required which will be formally updated and approved as required.

3.3. Tree Works

- 3.3.1. Once the pre-commencement site meeting has taken place then the following tree works must be undertaken by a qualified and insured tree surgery company.

Table 1. Table of tree works

Tree No.	Species	Proposed Works to Facilitate Development	Reason for Works
G1#	Holly and Laurel	No Action	-
T2#	Birch	No Action	-
T3#	Birch	No Action	-
T4#	Norway Maple	No Action	-
T5#	Norway Maple	No Action	-
T6#	Purple Norway Maple	Remove	To facilitate development
T7#	Cherry	Remove	To facilitate development

All tree works must be undertaken in line with BS3998:2010. Tree Work. Recommendations.

3.4. Site Briefing

- 3.4.1. Once the trees works have been completed to the recommended specifications and standards outlined in section 3.3, the Site Manager must ensure that all personnel who are to be working on this site are made fully aware of the constraints posed by the retained trees and that there are measures in place to protect these trees. I recommend making sure that all personnel have full access to the Arboricultural Method Statement and Tree Protection Plan (TPP), keeping a hard copy of this in the site office would also be advisable for reference.

3.5. Protective Fencing

3.5.1. Now that the site briefing has been completed, the protective fencing should be erected in the positions laid out in the Tree Protection plan which I have made available in appendix I.

3.5.2. The tree protection fencing will be appropriate to the degree and proximity of likely construction works. It is my opinion that in this instance, the default BS 5837:2012 tree protection fencing is disproportionate. I recommend that (if acceptable by the LPA) an adequate level of protection for the trees could be provided by 'Heras' type fencing, of welded mesh panels on rubber or concrete feet.

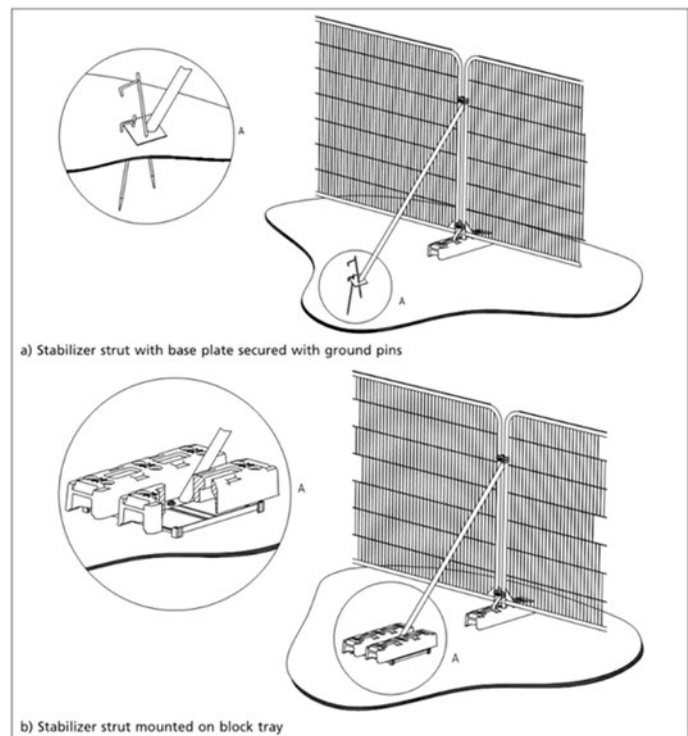


Figure 1. Tree protection fencing (Heras)

- 3.5.3. The fencing should be strong and suitable for local conditions. It should also take into account the degree of construction activity on the site.
- 3.5.4. Notices must also be erected on the fencing stating, 'Protected Area - No operations within fenced area'. I have made an example of a notice sign available in figure 2.



Figure 2. Tree protection notice to be fixed to protective fencing

- 3.5.5. Once the fence has been erected it should never be crossed and particular care should be taken not to store any materials or soil within the protected area.

3.6. Additional Precautions Outside Fenced Areas

- 3.6.1. Oil, bitumen, cement or other material likely to cause damage to the tree will not be stacked or discharged within 10m of the trees stem or within the protective area. Also, materials in general will not be stacked or discharged within the exclusion zone.
- 3.6.2. Concrete mixing and washing will not be carried out within 10m of any retained trees.
- 3.6.3. Fires will not be lit beneath the foliage or in a position where the flames could extend to within 5m of the foliage, branches or trunk. If the fire is large, then this may necessitate a distance of at least 20m.
- 3.6.4. Trees that are to be retained will not be used as anchorage for equipment.
- 3.6.5. Notice boards, telephone cables, or other services will not be attached to any part of the retained tree.
- 3.6.6. Care should be taken when using cranes or other equipment near the canopy of the retained trees. Also, any trees to be felled in proximity to the retained trees should be done so with particular care.

3.7. Cellular Confinement System

- 3.7.1. The use of a cellular confinement system will be utilised to create the hardstanding adjacent to T5# without having adverse effects. This will take place before any building works has begun onsite to protect the existing root system.
- 3.7.2. A cellular confinement system provides a load transfer mattress which prevents direct loads on tree roots and reduces the bearing pressure on subsoil's by stabilising aggregate surfaces against rutting under wheel loads. Figure 3 shows a side view of the cellular confinement system.



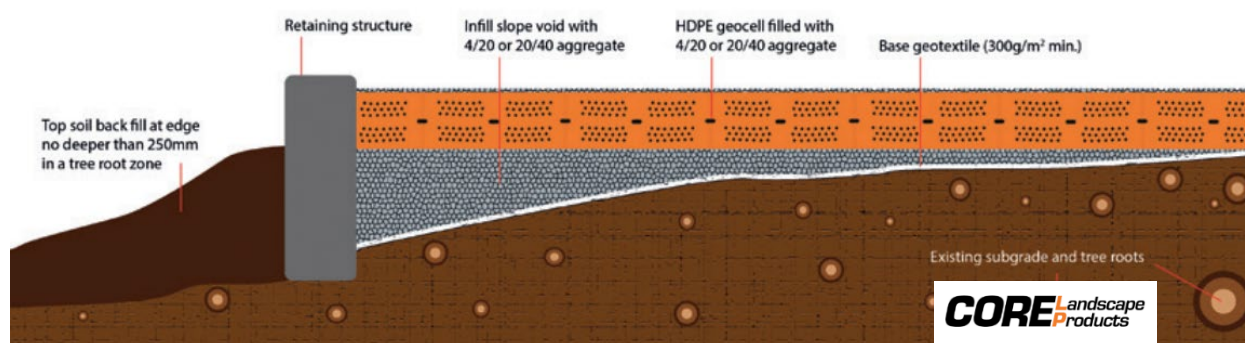


Figure3. A side view of a cellular confinement system courtesy Core LP (for more details visit <https://www.corelp.co.uk/core-tree-root-protection/>)

- 3.7.3. Edging is not required for the stability of the cellular confinement system, but it is necessary to retain the wearing course and the filling of incomplete cells at the edge of a surface. Kerb stones set in concrete haunching's dug into the ground are typical edging for standard surfaces but this method of installation is not suitable in this instance. An appropriate edging will be selected such as peg and board edging.
- 3.7.4. I have created the following methodology which lists the sequence of operations in order, necessary to complete the hardstanding with the minimum damage to the trees proposed for retention:
- Surface layer such as grass or gravel to be scraped off for levelling purposes. This can be done either by hand or by very small machinery to a maximum depth of 50mm.
 - Spread a thin layer of 4/20 or 20/40 aggregate material over the length of the proposed hardstanding area to fill any small rut and to level area.
 - Lay base geotextile material with at least 30cm overlaps. It is recommended that the base geotextile is made of polypropylene or polyester (min. 300g/m²) with a CBR puncture resistance of 4000N.
 - Extend the cellular confinement systems over the area of the proposed hardstanding.
 - Fill the voids within the Geoweb with a 4/20 or 20/40 aggregate material working into the voids. Help settlement of the stone by a minimum of four passes of a smooth roller (max. weight of 1000kg/m width without vibration), or alternatively by several passes with a tracked excavator
 - Install peg and board edge supports of other approved edging.
 - Lay an upper layer of geotextile over the Cellular Confinement System. The upper geotextile is required for protecting the infill matrix; this can be of the same thickness as the base layer or slightly thinner (100–300g/m²)

- Construct finished permeable surface as required in line with guidance illustrations below

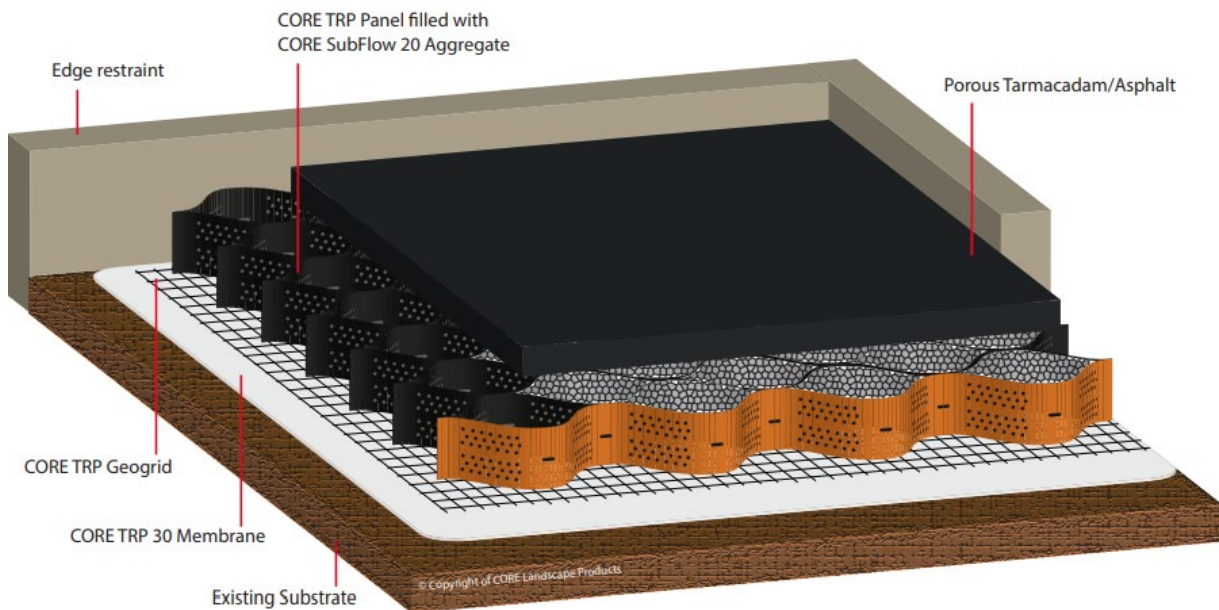



Appendix I



Tree Removal Plan & Tree
Protection Plan



Do not scale this drawing (printed or electronic version).
Contractors must check all dimensions from site.
This drawing is for use on this site only and should be used in conjunction with all relevant consultants drawings.

LEGEND



-  Retained Trees
-  Removed Trees
-  Root Protection Areas
-  Position estimated on site




Scale:	1:200 @ A1	Date:	13/10/2023
Job:	LTM0907.AIA.01		
Address	Smithy View Garage, Chester Road, LL12 8DY		
Client:	Mr Nick Dodman.		
Drawing Number:	LTM0907.TRP.02		
Drawn by:	Matthew Lally		

TREE REMOVAL PLAN




Do not scale this drawing (printed or electronic version).
Contractors must check all dimensions from site.
This drawing is for use on this site only and should be used in conjunction with all relevant consultants drawings.


LEGEND

 Retained Trees

 Root Protection Areas

 Protective Fencing (Metal)

 Cellular Confinement System

 Position estimated on site



Scale: 1:200 @ A1

Date: 13/10/2023

Job: LTM0907.AIA.01

Address: Smithy View Garage,
Chester Road,
LL12 8DY

Client: Mr Nick Dodman.

Drawing Number: LTM0907.TPP.02

Drawn by: Matthew Lally

TREE PROTECTION PLAN
