



Arboricultural Method Statement to BS5837:2012

Owen Ellis Architects.

**Yew Tree Cottage,
Moss Road,
Moss Valley,
Wrexham,
LL11 6HA.**

05 May 2023

Alan Thompson FdSc (Arb) MArborA

Table of Contents

If this report has been released electronically the appendices referred to herein can be found in the annexed zip folder/s as .pdf files. If this report has been released in hard copy the appendices will be bound into the back of this report. Plans are annexed separately as A0, A1, A2 or A3 as appropriate.

Introduction	3
Executive Summary	4
General Information.....	5
Tree Survey.....	6
Arboricultural Impact Assessment.....	7
Arboricultural Method Statement.....	9
Tree Works	10
Protected Species.....	12
Site Management.....	14
Prohibition	15
Sequencing of works.....	16
Protective Measures	17
Demolition	19
Construction.....	20
Landscaping.....	21
Monitoring and Supervision.....	22
Appendix 1: Tree Survey Schedule	24
Appendix 2: Tree Protection Notice.....	29
Appendix 3: Contact Details	31
Document Production Record	32

Introduction

Arbtech Consulting Limited (Arbtech) received written instruction in August 2022 from Owen Ellis Architects to attend Yew Tree Cottage, Moss Lane, Moss Valley, Wrexham, LL11 6HA (site) to undertake an arboricultural survey a to BS5837:2012 guidance to assess trees, hedges and major shrub groups growing on and within influencing distance of the site and to produce a Schedule of trees, Tree Constraints Plan, Arboricultural Impact Assessment, Arboricultural Method Statement and Tree Protection Plan.

Site location



Figure 1: OS Map (Bing Maps)



Figure 2: Aerial Image of site with approximate red line boundary (Bing Maps)

Executive Summary

This report describes the extent and effect of the proposed development at the site on individual trees and groups of trees within and adjacent to the site.

Trees within the site were surveyed; using a methodology guided by British Standard 5837:2012 'Trees in relation to design, demolition and construction – Recommendations' ("BS5837").


Subsequently, this report has been produced, balancing the layout of the proposed development against the competing needs of trees. This report comprises all of the requisite elements of an arboricultural implications assessment, method statement and supporting plans.

Checklist for Submission to Local Planning Authority

Tree survey	☒
Tree constraints plan	☒
Arboricultural impact assessment	☒
Arboricultural method statement	☒
Tree protection plan	☒

This report and its appendices follow precisely the strategy for arboricultural appraisal intended to provide local planning authorities with evidence that trees have been properly considered throughout the development process.

Proposal

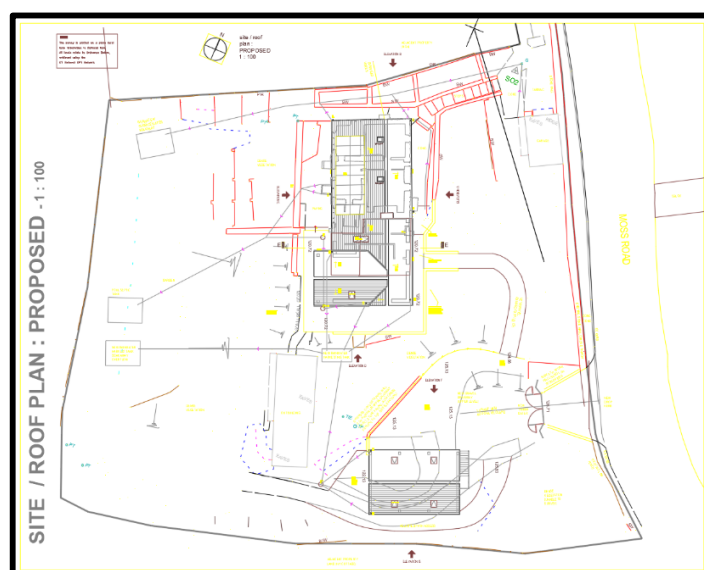

General Information

Client: Owen Ellis Architects

Site: Yew Tree Cottage, Moss Lane, Moss Valley, Wrexham, LL11 6HA

Brief proposal description: Extension of existing residential property & construction of detached garage, and associated landscaping.

Table 1: Documents referred to.

Document	Reference No.
Topographical Survey	21G36
Proposed layout drawing	4228 SK10
Landscape master plan drawing	N/A
LPA pre-app comments	N/A
British Standard 5837:2012	"BS5837"
Arboricultural Impact Assessment	Arbtech AIA 01
Tree Protection Plan	Arbtech TPP 01

Tree Survey

Survey: An arboricultural survey to BS5837 of all trees within impacting distance of the site was undertaken by Alan Thompson of Arbtech Consulting on 1st September 2022.

A total of 15 No. individual trees and 7 No. group of trees were surveyed. Details for each of the trees surveyed are provided in the Schedule of Trees (see Appendix 1)

Table 2: Documents upon which this tree survey has been based

Document	Originator	Reference Number	Title
Survey Base Plan	Survey Operations	21G136/001	Topographical Survey

Limitations: The survey was made at ground level using visual observation only. Detailed examinations, such as climbing inspections and decay detection equipment were not employed, though may form part of the survey's management recommendations. Measurements were taken using specialist tapes, laser and GPS devices. Where this was not possible, measurements are estimated.

Scope: Pre-development tree surveys make arboricultural management recommendations based exclusively upon the individual tree or group of trees condition relative to their present context (*i.e. not in relation to the proposed development*).

Legal Status: No statutory protection check has been performed. BS5837 does not draw any distinction between trees subject to statutory protection, such as a Tree Preservation Order ("TPO"), and those trees without. This is principally because a detailed planning consent overrides any TPO protection. Consequently, we do not seek to offer any comparison between or infer any difference in the quality or importance of TPO trees and other trees.

* For more information on the surveyed trees please see Arbtech Consulting Ltd, Tree Survey Schedule (Appendix 1), Tree Survey Report and Tree Constraints Plan.

Arboricultural Impact Assessment

Table 3: Documents upon which this assessment has been based

Document	Originator	Reference Number	Title
Survey Base Plan	Survey Operations	21G136/001	Topographical Survey
Proposals	Owen Ellis Architects	4228 SK10	Site/Ground Floor Proposed

There are a number of issues that may need to be addressed in an arboricultural impact assessment between the trees and the proposed development, these are as follows:

- The effect and extent of the proposed development within the root protection areas (RPAs) of retained trees;
- The potential conflicts of the proposed development with canopies of retained trees; and
- The likelihood of any future remedial works to retained trees beyond which would have been scheduled as a part of usual management.

Table 4: Impacts upon the RPAs of retained trees

Tree Number	Species	Structure	Incursion
T8	Sycamore	Gravel garden path	RPA
T9	Sycamore	Gravel garden path	RPA
T11	Prunus sp.	Services	RPA
T15	Myrobalan plum	Garden wall	RPA
G4	Goat willow	Goat willow	RPA

These impacts can be seen on the Arboricultural Impact Assessment drawing number Arbtech AIA 01.

Trees to be removed

The proposal requires the removal of 3 No. trees & 2 No. groups of young trees/shrubs.

A breakdown of all tree removals and pruning works can be seen in Table 8: Summary of Tree Works

Table 5: Number of individual trees to be removed.

U	A	B	C
0	0	1	2

Table 6: Number of groups to be removed. () represents partial removal of group.

U	A	B	C
0	0	0	2 (0)

Mitigation replacement tree planting will form part of the landscape proposal for the project.

Arboricultural Method Statement

The purpose of this method statement is to demonstrate how any aspect of the development that has potential to result in loss or damage to a tree may be implemented and provide an adequate level of protection for those trees that are to be retained during the proposed works.

Details of key site personnel, including site / project manager will be submitted to the Council's Tree Officer prior to the commencement of site works.

This method statement is to be approved and agreed to in writing by all key personnel prior to the commencement of site works.

No site personnel are to be present and no demolition, site clearance, building work or delivery of materials is to occur until the protective measures are in accordance with this method statement and the Tree Protection Plan drawing number Arbtech TPP 01.

Protective measures should be in accordance with this method statement and the Tree Protection Plan; drawing number Arbtech TPP 01 will remain unaltered and in situ, unless otherwise specified, for the entire duration of the construction.

Table 7: Documents upon which this assessment has been based

Document	Originator	Reference Number	Title
Survey Base Plan	Survey Operations	21G136/001	Topographical Survey
Proposals	Owen Ellis Architects	4228 SK10	Site/Ground Floor Proposed

Tree Works

For reasons of public safety, all tree works referred to herein must be carried out prior to any site personnel commencing works or any building materials being delivered.

Table 8: Summary of Tree Works

No.	Species	Works	Category
T12	Oak	Fell to ground level, remove stump	B2
T13	Sycamore	Fell to ground level, remove stump	C1
T14	Prunus	Fell to ground level, remove stump	C1
G5	Oak	Fell to ground level, remove stumps	C2
G6	Various	Fell to ground level, remove stumps	C2

Notes

All tree work is to be undertaken in accordance with British Standard BS 3998:2010, Recommendations for tree work. All arising's are to be removed and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber Lorries, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.

Tree removal

A tree should be felled in one piece only when there is no significant risk of damage to people, property or protected species (see Annex A).

Where restrictions (e.g. lack of space, buildings, other features, land ownership or use, or other trees which are to be retained) cannot be overcome, trees should be dismantled in sections.

This also applies where a tall stump is being retained but where branches are to be removed/pruned.

Extensively decayed trees can be unpredictable when they are being felled, and special precautions should therefore be taken, such as the use of a winch to guide the direction of fall.

Stump removal – stump grinding

Stump grinding should be to a minimum of 300mm deep or to extend through the base of the stump leaving the major roots disconnected if the intention is to reduce the potential for the spread of Honey fungus.

The grinding residue should be treated as arising's and removed from site.

NOTE Mechanical destruction of a stump by stump grinding is less disruptive to the site than digging out.

The hole left by stump removal, should be filled with soil or other material. The filling should be appropriate for future site usage, and for any surface treatment that is to be installed.

Where future plant growth is desired, the backfill material should be firmed in 150 mm layers by treading, avoiding excessive compaction and destruction of the soil structure.

Stump removal - digging

Stump removal by digging out should include disposal/utilisation of woody material (see Clause 13).

NOTE Whether done by hand or machine, digging out can cause severe disturbance of the site.

Where possible, when winching out a stump, a ground or other type of anchor should be used rather than a tree to be retained. If there is no alternative to using such a tree as an anchor, appropriate protective measures should be adopted.

After stump removal

The hole left by stump removal, whether by digging out or grinding, should be filled with soil or other material. The filling should be appropriate for future site usage and for any surface treatment that is to be installed.

Where future plant growth is desired, the back fill material should be firmed in 150mm layers by treading, avoiding excessive compaction and destruction of the soil structure.

Protected Species

Conservation Status of British Bats

The general consensus in Britain and Europe is that virtually all bat species are declining and vulnerable. Our understanding of population status is poor as there is very little historical data for most bat species. Certain species, such as the horseshoe bats, are better understood and have well documented contractions in range and population size.

Given this general picture of decline in UK Government within the UK Biodiversity Action Plan has designated five species of bats as priority species (greater and lesser horseshoe bats, barbastelle, Bechstein's and pipistrelle). These plans provide an action pathway whereby the maintenance and restoration of the former populations levels are investigated.

Legal Status of British Bats

Given the above position all British bats as well as their breeding sites and resting places enjoy national and international protection.

All bat species in the UK are fully protected under the Wildlife and Countryside Act 1981 (as amended) through inclusion in Schedule 5. All bats are also listed on Annex IV (and some on Annex II) of the EC Habitats Directive giving further, European protection. Taken together the act and Conservation of Habitats and Species Regulations 2012 (as amended)* make it an offence to; intentionally or deliberately kill, injure or capture (take) bats;

- Deliberately disturb bats (whether in a roost or not);
- Damage, destroy or obstruct access to bat roosts;
- Possess or transport a bat or any part of a bat, unless acquired legally;
- Sell, barter or exchange bats, or parts of bats

The legislation although not strictly affording protection to foraging grounds does protect roost sites. Bat roosts are protected at all times of the year whether or not bats are present. Any disturbance of a roost due to development must be licenced.

**the regulations that delivered by the UK's commitments to the Habitats Directive.*

Breeding birds

All nesting birds are protected under the Wildlife and Countryside Act (as amended) 1981, which makes it an offence to intentionally kill, injure or take any wild bird or take, damage or destroy its nest whilst in use or being built, or take or destroy its eggs. Furthermore a number of birds enjoy further protection under that Act and are listed on Schedule 1 of the Act. These further protected birds are also protected from disturbance and it may be necessary to operate “no-go” buffer zones around such nests – typically out to 100m.

Planning policy guidance on the treatment of species identified as priorities under the biodiversity action programme suggests that local authorities should take measures to protect the habitats of these species from further decline through policies in local development documents and should ensure that they are protected from the adverse effects of development, where appropriate, by using planning conditions or obligations. The conservation of these species should be promoted through the incorporation of beneficial biodiversity designs within developments.

Site Management

The site manager will be responsible for briefing and inducting all personnel who will be working on any stage of this development and especially those who will be working within or adjacent to the canopies or RPAs of retained trees; and will make them aware of, and provide a copy of this method statement and tree protection plan drawing number Arbtech TPP 01; this is to include but not exclusively of the movement and or operation of plant, excavations, unloading deliveries, mixing and or pouring of cement and concrete.

The site manager will be responsible for the day to day running and protection of all retained trees and for liaising with the project arborist about any tree related matters and prior to any works that may or will affect the RPAs or canopies of retained trees; this is to include but not exclusively the movement and or operation of plant, excavations, unloading deliveries, mixing, pouring and storage of all caustic materials that may cause harm to retained trees.

Any incidents of damage to retained trees or of tree protection measures will be documented by the site manager who will then report these incidents to the project arboriculturist immediately and make sure that works within this area cease until the project arborist has had an opportunity to inspect the damage and where appropriate, agree a mitigation plan with the local planning authority tree officer.

The site manager may designate another person to take charge of briefing and inducting process of new site personnel or visitors in his absence.

If the site manager is replaced or is absent from site for more than three consecutive working days the project arborist will be informed and a pre start meeting will be held with the new or acting site manager.

It is the responsibility of the site manager to ensure that the planning conditions attached to the planning consent are adhered to at all times and that a monitoring regime and supervision of any works within or adjacent to the RPAs are adopted.

If at any time pruning works are required other than those previously approved, permission must be sought from the LPA tree officer and once permission is granted they are to be carried out by a suitably qualified person in accordance with BS3998:2010 Tree work – Recommendations.

Prohibition

- Mechanical digging or scraping is not permitted within a defined root protection area or within areas cordoned off by protective barrier fencing.
- No access will be permitted within the protected areas;
- No materials, equipment or debris will be stored within any of the fenced areas, or against the fencing;
- Fires are not permitted within 10m of any vegetation.
- Leaning objects against or attaching of objects to a tree is not permitted.
- Machinery, plant and vehicles are not permitted to be washed down within 10m of vegetation.
- Chemicals and materials are not to be transported, stored, used or mixed within a root protection area or within areas cordoned off by protective barrier fencing.
- Cement silos, mixing site to be situated within a bunded area to prevent spillage/leaking of chemicals harmful to trees. These areas are to be sited well clear of protected trees.
- Refuelling of plant or machinery is prohibited within 10m of the construction exclusion zones.
- It is essential that allowance should be made for the slope of the ground so that damaging materials such as concrete washings, mortar or diesel oil cannot run towards trees.
- Where machinery is to be used within 5m of retained tree canopies a banks man will be required at all times whilst setting up, moving or operating within this distance of retained trees canopies.
- Storage of all caustic material and chemicals are to be situated well clear of protected areas and preferably on lower ground if slopes are present, or to be situated within a bonded area to prevent any spills or leaks entering the ground.

Sequencing of works

A logical sequence of events is to be observed and shall be phased as follows.

Table 9: Sequence of Events

Stage	Event
Stage 1	Pre-commencement site meeting
Stage 2	Carry out tree works as specified within the summary of tree works
Stage 3	Installation of protective measures in accordance with the approved tree protection plan/s
Stage 4	Site set up for construction
Stage 5	Undertake and complete construction works
Stage 6	Undertake external landscaping works outside of the construction exclusion zones
Stage 7	Removal of all machinery and materials from site
Stage 8	Dismantle and removal of protective measures
Stage 9	Undertake external landscaping works within the construction exclusion zones
Stage 10	Sign off from project arboriculturist

Protective Measures

Protective measures are to be installed immediately following the completion of the tree works, and are to be sited and aligned in accordance with the tree protection plan (Arbtech TPP 01) prior to the commencement of any works or the introduction of any machinery or material to site.

Upon installation of the protective measures around the retained trees the project arboriculturist will visit the site to inspect and document the position and specifications of the protective measures.

In the event that the protective measures and their positions do not comply with this arboricultural method statement document number Arbtech AMS 01 (05-05-23) and tree protection plan drawing number Arbtech TPP 01, the project arboriculturist shall inform the client and fencing contractor so adjustments can be made.

When the protective measures comply with document number Arbtech AMS 01 (05-05-23) and tree protection plan drawing number Arbtech TPP 01, the project arboriculturist will sign off the protective measures in writing to the client and will send a copy to the fencing contractor, site agent and local authority tree officer.

If the protective measures become damaged or there is any accident or emergencies involving trees, these areas are to be cordoned off immediately with high visibility plastic mesh fencing. The site agent is to photograph and document the damage and inform the project arboriculturist immediately after the incident and all work within in this area is to cease until the project arboriculturist has made a visit to the site. Any and all damaged sections of protective measures shall be replaced within 48 hours of the initial incident.

The protected area is sacrosanct and will not be invaded by the storage of materials, mixing of concrete or other products, accessed by machinery, equipment or pedestrians or in any other way disturbed by construction activity.

The protective measures will remain in place until the completion of stage 8 (see Sequencing of Works), thereafter they will be carefully dismantled only with the agreement of the project arboriculturist and or the local authority tree officer.


The existing site boundary measures are to be retained for the duration of the development. If for any reason the existing boundary measures are not to be used protective barrier fencing is to be installed along the line of the boundaries and is only to be removed upon the written permission of the project arboriculturist or LPA tree officer upon the completion of the development or immediately prior to the installation of the permanent boundary measures.

No equipment, vehicles or plant shall operate beyond the tree protection fencing. Booms, hoists and rigs should be kept as far away from the canopies of retained trees at all times. Where it is necessary to operate within 5m of a tree canopy, it will be done with the utmost caution and under the control of a banks man. Damage to trees will be considered a breach of this tree protection plan, which in turn could be a breach of planning permission.

Protective Barrier Fencing

Protective barrier fencing should be appropriate for the intensity and proximity of the development to protect trees where development activity is in proximity.

Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabiliser struts, which should be attached to a base plate and secured with ground pins.

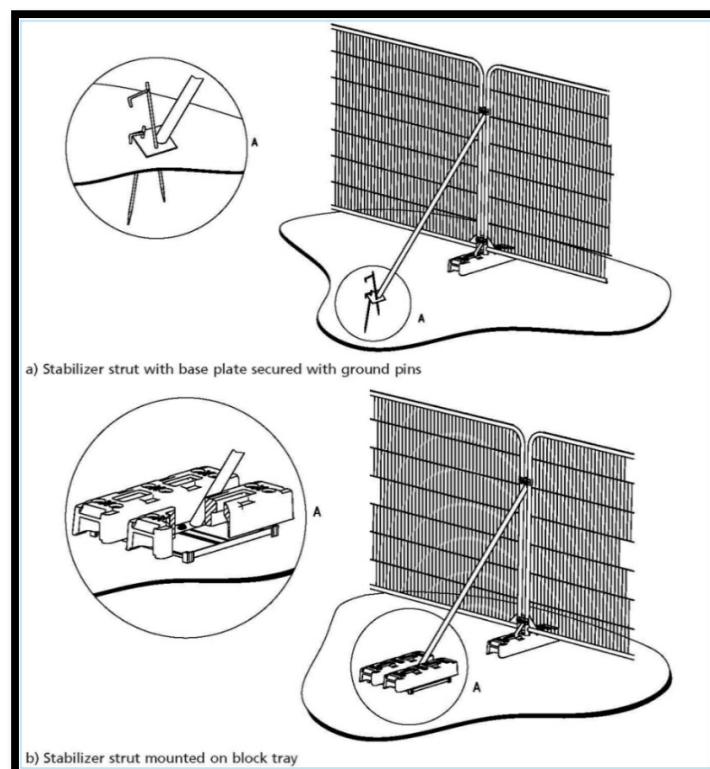

Signage denoting the words “*tree protection area*” at 5.0m intervals should be fixed to the protective barrier fencing (See Appendix 2).

Protective fencing is to be removed only with the written permission of the arboricultural consultant and approval of the local planning authority (LPA).

Demolition

Prior to the demolition of the existing site features, all tree works are to have been completed, tree protection measures are to be in place as per Arbtech Consulting Ltd. tree protection plan document number Arbtech TPP 01 and have been signed off and a copy of the demolition method statement has been submitted and approved by the project arboriculturist and LPA tree officer, to ensure that there is no conflict with this method statement.

Any demolition work within or immediately adjacent to RPAs or canopies of retained trees is to be undertaken under the direct on-site supervision of an arboriculturist.

Construction

Prior to the construction of the proposal, a copy of the construction method statement should have been submitted and approved by the project arboriculturist and LPA tree officer, to ensure that there is no conflict with this method statement.

Any excavations and construction work within or immediately adjacent to RPAs or canopies of retained trees is to be undertaken under the direct on-site supervision of an arboriculturist.

Garden footpath

The proposed gravel garden footpath situated within the RPAs of tree nos. T8 & T9 is to be designed in conjunction with arboricultural advice to ensure that the construction will be situated entirely above the existing soil level and will not require excavation into the RPA of the tree. The footpath will be porous.

Supervised Excavation

Excavation is required for three small areas within the RPAs of trees T11, T15 & G4 (all category C trees) for services & a garden wall, these excavations will be carried out under direct on-site arboricultural supervision to the required depth of the excavation.

The soil is to be loosened with the aid of a fork or pickaxe and then cleared with the aid of an Air-spade, Air-vac and or shovel. Any roots found will be cleanly severed by the arboricultural consultant with either a hand saw or secateurs.

Any roots found with a diameter of less than 25mm shall be cleanly severed by the arboricultural consultant. Any roots of 25mm and above shall be excavated around without damaging them; the arboricultural consultant shall decide if it's feasible or necessary to retain the root, if not it shall be severed.

The edge of the excavation closest to the trees will be covered with damp hessian to prevent soil collapse or contamination by concrete.

Landscaping

Any tree planting should take into consideration the available space for tree growth and development in order to ensure the trees are physically suited to the site at maturity. A specification for and notation relating to the precise alignment of replacement trees will be contained in the landscape proposals.

Landscaping around retained trees may only be carried out once all tree protection measures have been removed (planting, turfing, fencing etc.).

All excavations within the Root Protection Areas shall be undertaken by hand and without reducing current ground levels unless it is agreed in writing with the LPA. At no time is the use of a rotavator permitted within the RPAs of retained tree.

Any tree roots discovered will be left in-situ and shall not be cut or otherwise damaged. Where possible, the soil structure within the Root Protection area shall be preserved.

No works will be carried out within the RPAs of any trees if the soil moisture is of such a level that soil compaction may be likely. Should the soil become compacted or has poor structure which would hinder the development of the existing trees and plants or any new plantings the arboriculturist should be consulted about soil decompaction techniques.

Monitoring and Supervision

Where trees have been identified within this method statement and tree protection plan drawing number Arbtech TPP 01 for retention, there should be an auditable system of arboricultural monitoring. This is to extend to arboricultural supervision whenever demolition or construction activity is to take place within or adjacent to any canopy or RPA.

The development's tree protection measures are to be monitored and all demolition and construction works to be undertaken within or adjacent to the RPAs of retained trees are to be supervised by project arboriculturist, who should be retained to record and report observations to the council at appropriate intervals.

Pre-commencement site meeting

Prior to the commencement of any works or machinery and materials arriving on site a pre-commencement site meeting involving the project arborist, landowner or agent, site manager, contractors and engineer (as appropriate) and the relevant LPA officers will be held to ensure that all aspects of the arboricultural method statement and tree protection are understood and for all parties to swap contact details (see Appendix 3).

Monitoring and supervision schedule

The initial monitoring visit will be to check that the tree protective measures are in the correct location and as specified within the approved method statement; if so to sign off their installation.

There after monitoring visits are to take place at regular intervals, to ensure that tree protection measures are in place and are functioning as designed or whenever necessary to undertake works to be carried out under arboricultural supervision. The frequency of the monitoring visits is to be determined with the LPA tree officer at the pre-commencement site meeting.

A record of all arboricultural monitoring and supervision visits will be kept and any faults will be logged, this will then be copied to the site agent, developer and local planning authority in a digital format.

If during the course of the development it is necessary for areas to be re-designed so that they would require changes to the approved arboricultural method statement or tree protection plan and so affecting retained trees the project arborist and LPA tree officer will be invited to attend a site meeting with all relevant parties. Prior to any changes being implemented these must have been approved in writing by the LPA tree officer.

Supervision

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that are to be undertaken within or adjacent to the RPAs of all retained trees and will be advised a minimum of 72 hours prior to the commencement of any works that require his attendance, these will include:

1. Pre-commencement site meeting;
2. Location of protective measures;
3. Excavation for garden wall & services within the RPAs of trees T11, T14 & group G6.
4. Any excavations within and immediately adjacent to RPAs, including foundations, hard surfacing or underground services;

Completion meeting

Once all construction works have been completed all materials and machinery has been removed from site the project arborist shall be informed and will invite the LPA tree officer to meet on site to discuss the process and discuss any final remedial works that may be required and to sign the development off so that the protective measures may be removed.

Appendix 1: Tree Survey Schedule

BS5837:2012 Tree Survey

Artbech Consulting Ltd.

Client: Owen Ellis Architects
 Project: Yew Tree Cottage, Moss Road, Moss Valley, LL11 6HA.
 Survey Date: 01/09/2022
 Surveyor: Alan Thompson



Unit 3, Well House Barns
 Chester Road
 Chester
 Cheshire
 CH4 0DH
 Phone: 01244 66 11 70

Tree and Tag No Species		Hght (m)	Stems		Crown		Age	RP A (m²) R (m)	Phys Condition	Structural Condition	Preliminary Recommendations			Cat ERC
			No	Ø (mm)	Spread (m)	Clear (m)					Survey Comment			
G1												Estimated Measurements		
A Group		4	1	100	N	1.5	0.5	Y	A: 4.5 R: 1.19	Good	C: Good S: Good B: Good	Group is comprised of six ornamental shrubs and young trees. Species are holly, hazel, cordyline, viburnum and cypress. Measurements given are estimated averages for the group.	C.2	
- -					E	1.5	0.5						20 to 40 yrs	
					S	1.5	0.5							
					W	1.5	0.5							
G2												Estimated Measurements		
A Group		5	1	180	N	2.5	1	Y	A: 14.7 R: 2.16	Good	C: Good S: Good B: Good	Group is comprised of six young trees. Species are sycamore, elm and hawthorn.	C.2	
- -					E	2.5	1						>40 yrs	
					S	2.5	1							
					W	2.5	1							
G3												Estimated Measurements		
A Group		15	1	430	N	6.5	5.5	SM	A: 83.7 R: 5.16	Good	C: Good S: Good B: Good	Small oof site wooded area is comprised of approximately 15 semi mature trees. Species are predominantly sycamore interspersed with ash and goat willow. Measurements given are estimated averages for the group.	B.1.2	
- -					E	6.5	5.5						>40 yrs	
					S	6.5	5.5							
					W	6.5	5.5							
G4												Estimated Measurements		
Goat Willow		4.5	1	120	N	2.5	1	Y	A: 6.5 R: 1.43	Good	C: Good S: Good B: Good	Group is comprised of five young goat willow trees. Measurements given are estimated averages for the group.	C.2	
<i>Salix caprea</i>					E	2.5	1						>40 yrs	
					S	2.5	1							
					W	2.5	1							
Age Classifications:		N	Newly planted	EM	Early Mature	Condition:		C	Crown	Stems:		Ø	Diameter	
		Y	Young	M	Mature			S	Stem			(Eq)	Equivalent stem diameter using BS5837:2012 definition	
		SM	Semi-mature	OM	Over Mature			B	Basal area					

Tree and Tag No Species	Hght (m)	Stems		Crown		Age	RP A (m²) R (m)	Phys Condition	Structural Condition	Preliminary Recommendations Survey Comment	Cat ERC
		No	Ø (mm)	Spread (m)	Clear (m)						
G5										Estimated Measurements	
Common Oak <i>Quercus robur</i>	4.5	1	70	N	1.5	2	Y	A: 2.2 R: 0.83	Good	C: Good S: Good B: Good	C.2 >40 yrs
				E	1.5	2				Group is comprised of two young oak trees. Measurements given are estimated averages for the group.	
				S	1.5	2					
				W	1.5	2					
G6										Estimated Measurements	
A Group	3	1	80	N	1.5	0.5	Y	A: 2.9 R: 0.96	Good	C: Good S: Good B: Good	C.2 >40 yrs
--				E	1.5	0.5				Group is comprised of ornamental shrubs and young trees. Species include hawthorn, viburnum, hazel and elder. Measurements given are estimated averages for the group	
				S	1.5	0.5					
				W	1.5	0.5					
G7										Estimated Measurements	
Goat Willow <i>Salix caprea</i>	6.5	1	300	N	4.5	2	SM	A: 40.7 R: 3.59	Good	C: Good S: Good B: Good	B.2 >40 yrs
				E	4.5	2				Group is comprised of three semi mature goat willow and one young oak. Measurements given are estimated averages for the group.	
				S	4.5	2					
				W	4.5	2					
T1											
Common Oak <i>Quercus robur</i>	5.5	1	110	N	2	2	Y	A: 5.5 R: 1.32	Good	C: Good S: Good B: Good	C.1 >40 yrs
				E	1	2					
				S	2	2					
				W	2	2					
T2											
Douglas Fir <i>Pseudotsuga menziesii</i>	18.5	1	520	N	3.5	2	SM	A: 122.3 R: 6.23	Good	C: Good S: Good B: Good	B.1 >40 yrs
				E	4.5	2					
				S	5	2					
				W	4.5	3					
T3											
Western Red Cedar <i>Thuja plicata</i>	17	1	400	N	4.5	3	SM	A: 72.4 R: 4.8	Good	C: Good S: Good B: Good	B.1 >40 yrs
				E	3.5	3					
				S	3	4					
				W	4	3					
Age Classifications: N Newly planted EM Early Mature Condition: C Crown Stems: Ø Diameter Y Young M Mature S Stem (Eq) Equivalent stem diameter using BS5837:2012 definition SM Semi-mature OM Over Mature B Basal area											

Tree and Tag No Species		Hght (m)	Stems		Crown		Age	RP A (m²) R (m)	Phys Condition	Structural Condition	Preliminary Recommendations			Cat ERC
			No	Ø (mm)	Spread (m)	Clear (m)					Survey Comment			
T4														
Sycamore	10	1	390		N	3	3.5	SM	A: 68.8	Fair	C: Poor			C.1
Acer pseudoplatanus					E	3	3.5		R: 4.67		S: Fair	Excessive amount of squirrel damage was observed throughout tree's crown.	10 to 20 yrs	
				S	3	3.5				B: Good				
				W	3	3.5								
T5													Estimated Measurements	
Sycamore	14	2	537	(Eq)	N	5.5	4.5	SM	A: 130.7	Good	C: Good			B.1
Acer pseudoplatanus					E	5.5	4.5		R: 6.45		S: Ivy	Tree is growing in an inaccessible location, so could not be fully inspected and measurements given are estimated.	>40 yrs	
				S	5.5	4.5				B: Good				
				W	5.5	4.5								
T6														
Sycamore	12	1	390		N	4	6	SM	A: 68.8	Good	C: Good			B.1
Acer pseudoplatanus					E	5.5	4		R: 4.67		S: Good		>40 yrs	
				S	5.5	5				B: Good				
				W	5	6								
T7													Estimated Measurements	
Sycamore	16	6	637	(Eq)	N	6.5	7	M	A: 183.5	Good	C: Good			B.1
Acer pseudoplatanus					E	7	7		R: 7.64		S: Ivy	Thick ivy is spreading throughout tree's stems and lower crown precluding a full stem inspection.	>40 yrs	
				S	7	2				B: Good				
				W	7	6								
T8													Estimated Measurements	
Sycamore	15	2	484	(Eq)	N	4.5	8	SM	A: 106.1	Good	C: Fair			B.2
Acer pseudoplatanus					E	4.5	8		R: 5.81		S: Ivy	Tree's crown is becoming suppressed by neighbouring trees. Thick ivy is spreading throughout tree's stem and lower crown precluding a full stem inspection. Off site tree.	20 to 40 yrs	
				S	4.5	8				B: Good				
				W	4.5	8								
T9													Estimated Measurements	
Sycamore	17	1	480		N	5.5	5	SM	A: 104.2	Good	C: Good			B.1
Acer pseudoplatanus					E	7.5	5		R: 5.75		S: Good	Off site tree, measurements given are estimated. Thick ivy is spreading throughout tree's stem precluding a full stem inspection.	>40 yrs	
				S	6.5	8				B: Good				
				W	5	8								
Age Classifications:		N	Newly planted	EM	Early Mature		Condition:		C	Crown	Stems:		Ø	Diameter
	Y	Young	M	Mature					S	Stem			(Eq)	Equivalent stem diameter using BS5837:2012 definition
	SM	Semi-mature	OM	Over Mature					B	Basal area				

Tree and Tag No Species	Hght (m)	Stems		Crown		Age	RP A (m ²) R (m)	Phys Condition	Structural Condition	Preliminary Recommendations Survey Comment	Cat ERC
		No	Ø (mm)	Spread (m)	Clear (m)						
T10										Estimated Measurements	
Common Ash <i>Fraxinus excelsior</i>	10	6	441 (Eq)	N 7.5 E 7.5 S 7.5 W 7.5	5 4 6 5	SM	A: 88 R: 5.29	Decline	C: Poor S: Ivy B: Good	Off site tree. Ash dieback symptoms observed throughout tree's crown, 25% dieback of crown volume. Thick ivy is spreading throughout tree's stems precluding a full stem inspection.	C.1 10 to 20 yrs
T11											
Common or Black Elder <i>Sambucas nigra</i>	4	2	156 (Eq)	N 1 E 1.5 S 2 W 1.5	2 2 1.5 2	SM	A: 11 R: 1.87	Fair	C: Fair S: Ivy B: Good	Slight apical dieback observed in tree's upper crown. Thick ivy is spreading throughout tree's stem into lower crown precluding a full stem inspection.	C.1 10 to 20 yrs
T12											
Common Oak <i>Quercus robur</i>	7.5	1	290	N 4 E 3 S 4 W 4	2.5 4 2.5 2.5	Y	A: 38.1 R: 3.48	Good	C: Good S: Good B: Good	Early mature tree.	B.2 >40 yrs
T13											
Sycamore <i>Acer pseudoplatanus</i>	7	1	180	N 2.5 E 3 S 3 W 2.5	3 3 3 4	Y	A: 14.7 R: 2.16	Good	C: Good S: Good B: Good	Tree of limited amenity value.	C.1 >40 yrs
T14											
Prunus <i>Prunus Unknown</i>	4.5	1	120	N 2.5 E 2.5 S 2.5 W 2.5	2 2 2 2	Y	A: 6.5 R: 1.43	Good	C: Good S: Good B: Good	Tree of limited amenity value.	C.1 20 to 40 yrs
T15											
Myrobalan Plum <i>Prunus cerasifera</i>	5	1	260	N 2.5 E 3 S 3 W 3	2 2 2 2	SM	A: 30.6 R: 3.12	Fair	C: Fair S: Good B: Good	Tree's crown was sparse at time of survey, possibly as a result of drought conditions.	C.1 10 to 20 yrs
Age Classifications: N Newly planted EM Early Mature Condition: C Crown Y Young M Mature S Stem SM Semi-mature OM Over Mature B Basal area											
Stems: Ø Diameter (Eq) Equivalent stem diameter using BS5837:2012 definition											

Appendix 2: Tree Protection Notice

(To be printed at A3 or larger)

Tree Protection Area

KEEP OUT

Do not move this fence

(TOWN & COUNTRY PLANNING ACT 1990)

**TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND/OR
ARE THE SUBJECT OF A TREE PRESERVATION ORDER.**

**CONTRAVENTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL
PROSECUTION**

**ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION
OF THE LOCAL PLANNING AUTHORITY**



Arbtech Consulting Limited.
Unit 3, Well House Barn, Chester Road, Chester, CH4 0DH
<https://arbtech.co.uk> - 01244 661170

Appendix 3: Contact Details

Name	Position	Company	Contact
Will Barralet	Client	Owen Ellis Architects	https://www.owenellis.co.uk/
	Tree Officer		
Alan Thompson	Arboricultural Consultant	Arbtech Consulting Ltd.	01244 661170 07703 676216 at@arbtech.co.uk https://arbtech.co.uk
	Site Manager		
	Main contractor		

Document Production Record

Document number	Editor	Signature	Position	Issue number	Date
Arbtech AMS 01	Alan Thompson		Arboricultural Consultant	1	05/05/2023

Limitations

Arbtech Consulting Ltd has prepared this Report for the sole use of the above named Client/Agent in accordance with our terms of business, under which our services were performed. No other warranty, expressed or implied, is made as to the professional advice included in this Report or any other services provided by us. This Report may not be relied upon by any other party without the prior and express written agreement of Arbtech Consulting Ltd. The assessments made assume that the sites and facilities will continue to be used for their current purpose without significant change. The conclusions and recommendations contained in this Report are based upon information provided by others and upon the assumption that all relevant information has been provided by those parties from whom it has been requested. Information obtained from third parties has not been independently verified by Arbtech Consulting Ltd.

Copyright

© This Report is the copyright of Arbtech Consulting Ltd. Any unauthorised reproduction or usage by any person other than the addressee is strictly prohibited.
