

Arbor Vitae Environment Ltd

**Tree Condition Report
Arboricultural Impact Assessment
Method Statement
Tree Protection Plan and Root Protection Areas**

**Land at Forge Farm, Pont-y-blew,
Chirk**

For Parrys



06.08.2018

By

Zoe Adlington BSc Hons MArborA

for

Arbor Vitae Environment Ltd

Contents

- 1.0 Remit
- 2.0 Report Limitations
- 2.1 Statutory Obligations
- 2.2 Individual Tree Condition Survey, Arboricultural Impact Assessment, Root Protection Areas and Method Statement
- 3.0 Method statement Summary
- 3.2 Summary of Works
- 3.3 Tree protection specification

Appendix 1

Photo Detail: Tree condition illustration ref. Sect 2.2

Appendix 2

Tree Protection Plan and RPA

Appendix 3

BS 5837 2012 Protection illustrations x2

Appendix 4

Appendix 4 Glossary of Arboricultural Terms

1.0 Remit:

Check the condition of trees identified on the Site Drawing provided by Parrys within and adjacent to the proposed development area. Provide an Arboricultural Impact Assessment, Method Statement and Tree Protection Plan to BS5837 (2012) Trees in relation to design, demolition and construction – Recommendations.

.0 Report limitations:

The conclusion and recommendations in this report are valid for a period of one year, or a lesser period where indicated in the report. All trees are susceptible to exceptional weather events or deterioration resulting from other environmental changes in close proximity to the tree. The evaluation is based upon Visual Tree Assessment (Mattheck & Breloer 2001). Observations have been made from ground level with the aid of binoculars.

.1 Statutory Obligations

Bats and the Law (Woodland Management for Bats 2005)

'The Wildlife and Countryside Act 1981 makes it an offence to disturb, damage or destroy bats or their roosts. The Act applies in both England & Wales and requires consultation with the appropriate SNCO before carrying out activities which might harm or disturb bats or their roosts. The Act is amended by the CROW Act 2000. This adds *recklessness* to the offence of damaging or destroying a place a bat uses for shelter, or disturbing a bat while using a roost.

The Conservation (Natural Habitats Regulations 1994) implements the European Directive 92/43/EEC on the Conservation of Natural Habitats and of Wild Fauna and Flora 1992, amended August 2007 & Oct 2010. Under the regulations, damaging or destroying a breeding site or resting place is an absolute offence, regardless of whether the act of doing so may be regarded as reckless, deliberate or accidental.

Wild Birds (Mynors 2002) The Primary legislation affecting wild birds in England, Scotland and Wales is the Wildlife and Countryside Act 1981 (as amended). In January 2001 the Countryside and Rights of Way Act 2000 (CROW) included amendments, which strengthened the law in England and Wales. The basic principle of the Wildlife and Countryside Act 1981 (as amended) is that all wild birds, their nests and eggs, are protected by law and some rare species are afforded special protection. There are certain exemptions to this notably in respect of wildfowl, game birds and various species that may cause damage. (Cowan 2002)

Felling licence: Subject to tree size, location, condition and other Statutory protection, or prior planning approval, not more than 5m³ of timber can be felled in any Calendar quarter without first obtaining a Forestry Commission (FC) felling licence. Failure to obtain a licence where required is a prosecutable offence. Detailed information including exemptions can be found on the FC web site

Conservation Area and Tree Protection Orders: The Local Authority protects trees within the district by the use of and administration of Tree Preservation Orders (TPOs). Trees can also be protected if they are within a Conservation Area. TPOs are used to protect trees (including areas of woodland) where their removal would have a significant impact on the local environment and its enjoyment by the public. TPOs prohibit the cutting down, uprooting, wilful damage or destruction of trees. Any works to a tree(s) protected by a TPO or falling within a Conservation Area first requires the consent of the Local Authority.

It is a prosecutable offence to carry out work to a tree protected by a TPO, or remove it, without the prior consent of the Local Authority. Detailed information including exemptions can be found on the Local Authority web site

.2 Tree Condition Survey and Arboricultural Impact Assessment (AIA)

Inspection method: Visual Tree Assessment (VTA) from ground level.

Location: Land at Forge Farm, Pont-y-blew, Chirk. **Date:** 6th August 2018

Visited: 6th August 2018

Protection Status: Not known at the time of the survey

Limitations: Trees and shrubs have been identified, current height measured to the nearest metre and ultimate height assessed with reference to The Hillier Manual of Trees and Shrubs. A Visual Tree Assessment (VTA) has been carried out on trees in, or adjacent to, the development site. Refer to proposed site layout drawing for tree locations. The risk assessment and recommendations are valid for a period of one year. No detection equipment has been used other than a sounding hammer and metal probe.

NB. All trees are at risk of failure through exceptional weather conditions.

Identification No.	T1
Species	Apple spp. <i>Malus spp.</i>
Current Height (M)	7m
Ultimate Height (M)	7m
Current Stem Dia (cm)	38cm
Crown clearance	4m
Crown Spread (M)	Radius: 3m
Growth stage	Mature
Tree Condition: Root: no soil movement. Stem: extensive brown rot decay within the stem. Decayed heartwood exposed. Crown: No evidence of recent breakouts or significant dieback. Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 Category B2: Trees present in number, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals. Water Demand NHBC 4.2-B: moderate Root Protection Area RPA: for tree of 38cm diameter at 1.5m $(0.38 \times 12) = 4.6\text{m}$. Total RPA required at current stage of growth = 66.4m^2 Arboricultural Impact Assessment AIA: - The proposed access falls outside the RP of T1 - No trench excavation permitted within the RPA of T1 Method Statement: Construction of new access - The existing hedge acts as an adequate barrier from the construction site.	

Identification No.	T2
Species	Apple spp. <i>Malus spp.</i>
Current Height (M)	4m
Ultimate Height (M)	6m
Current Stem Dia (cm)	33cm
Crown clearance	2m
Crown Spread (M)	Radius: 3.5m
Growth stage	Mature
Tree Condition: Root: no soil movement. Stem: stem is hollow due to extensive brown rot. Crown: No evidence of recent breakouts or significant dieback. Tree Quality Assessment: Ref.BS5837 (2012) 4.5. Category B2: Trees present in number, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals. Water Demand NHBC 4.2-B: Moderate Root Protection Area RPA: for tree of 33cm diameter at 1.5m $(0.33 \times 12) = 4.0\text{m}$. Total RPA required at current stage of growth = 50m^2 Arboricultural Impact Assessment AIA: - The proposed access falls outside the RPA of T2 - No trench excavation is permitted within the RPA Method Statement: Construction of new access - The existing hedge acts as an adequate barrier from the construction site.	

Identification No.	T3
Species	Common ash <i>Fraxinus excelsior</i>
Current Height (M)	21m
Ultimate Height (M)	21m
Current Stem Dia (cm)	120cm
Crown clearance	8m
Crown Spread (M)	8m
Growth stage	Over mature
Tree Condition: Root: no soil movement. Stem: the main stem has broken out. Large vertical crack down the remaining portion of the central stem. two first order limbs attached to central stem are likely to cause the failure of the remaining stem by splitting in half. Crown: no recent breakouts or significant dieback. Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 Category C1: 'Trees of impaired condition that they do not qualify in higher categories' Water Demand NHBC 4.2-B: Moderate Root Protection Area RPA: for tree of 120cm diameter at 1.5m (1.2 x 12) = 14.4m. Total RPA required at current stage of growth = 651m² Arboricultural Impact Assessment AIA: • The proposed development falls outside the RPA of T3 • No trench exaction permitted within the RPA • Stem at risk of splitting and remaining crown collapsing on the proposed hedgerow. Method Statement: Proposed access and camping pods • Tree proposed for removal due to declining condition.	

Identification No.	Part of G1- T4
Species	Common alder <i>Alnus glutinosa</i>
Current Height (M)	19m
Ultimate Height (M)	20m
Current Stem Dia (cm)	37cm
Crown clearance	2m
Crown Spread (M)	Radius: 3.5m (on development side)
Growth stage	Early mature
Tree Condition: Root: no soil movement. Stem: no visual evidence of significant defects. Crown: No evidence of recent breakouts or significant dieback Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 Category B2: Trees present in number, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals. Water Demand NHBC 4.2-B: Moderate Root Protection Area RPA: for tree of 37cm diameter at 1.5m $(0.37 \times 12) = 4.4\text{m}$. Total RPA required at current stage of growth = 61m^2 Arboricultural Impact Assessment AIA: - The proposed camping pods and associated access fall outside the RPA of G1 - No trench excavation permitted within the RPA Method Statement: Construction of new camping pods and associated access - Install the section of Heras fence barrier positioned as indicated on the tree protection plan. Specified as recommended in BS5837 (2012) fig 3 appended.	

Identification No.	Part of G1 - T5
Species	Common ash <i>Fraxinus excelsior</i>
Current Height (M)	19m
Ultimate Height (M)	21m
Current Stem Dia (cm)	19cm and 28cm
Crown clearance	2m
Crown Spread (M)	Radius: 3.5m
Growth stage	Mature
Tree Condition: Root: no soil movement. Stem: wounds occluded Crown: No evidence of recent breakouts. Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 Category B2: Trees present in number, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals. Water Demand NHBC 4.2-B: Moderate Root Protection Area RPA: for tree of 19cm and 21cm diameter at 1.5m $\sqrt{(0.19^2 + 0.21^2)} \times 12 = 4.1\text{m}$. Total RPA required at current stage of growth = 53m^2 Arboricultural Impact Assessment AIA: - The proposed camping pods and associated access fall outside the RPA of G1 - No trench excavation permitted within the RPA Method Statement: Construction of proposed camping pods and associated access - Install the section of Heras fence barrier positioned as indicated on the tree protection plan. Specification as recommended in BS5837 (2012) fig.3 appended	

Identification No.	Part of G1- T6
Species	Common alder <i>Alnus glutinosa</i>
Current Height (M)	19m
Ultimate Height (M)	20m
Current Stem Dia (cm) at 1.5m	45cm
Crown clearance	5m
Crown Spread (M)	Radius: 7m
Growth stage	Young
Tree Condition: Root: no soil movement. Stem: wounds occluded Crown: No evidence of recent breakouts or significant dieback. Minor deadwood in crown. Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 Category B2: Trees present in number, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals. Water Demand NHBC 4.2-B: Moderate Root Protection Area RPA: for tree of multiple diameters at 1.5m (0.45×12) = 5.4m . Total RPA required at current stage of growth = 92m ² Arboricultural Impact Assessment AIA: - The proposed access and camping pods fall outside the RPA of T6 - No trench excavation is permitted within the RPA Method Statement: construction of proposed camping pods and associated access - Install the section of Heras fence barrier positioned as indicated on the tree protection plan. Specification as recommended in BS5837 (2012) fig.3 appended	

H1:

Condition: 60m of managed hawthorn, sycamore, ash and hazel hedge, forming a 2.5m high screen. No evidence of recent breakout or significant dieback.

Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 **Category B2:** 'Trees present in numbers, usually growing as groups or woodlands, such that they collect a higher collective rating'.

Water Demand NHBC 4.2-B: High

Root Protection Area RPA: for average tree of 10cm diameter at narrowest point below fork (0.15×12) = **1.8m** radius.

Total RPA required at current growth stage = 10.2m²

Arboricultural Impact Assessment AIA:

- 40m section of H1 is proposed for removal in order to create adequate visibility splay for entrance to site.
- No trench excavation permitted within the RPA of remaining hedge

Method Statement: construction of new access and dwelling

- Install the section of Heras fence barrier positioned as indicated on the tree protection plan. Specification as recommended in BS5837 (2012) fig.3 appended.
- 40m section of H1 proposed for removal by the developer.

H2:

Condition: 40m of managed hawthorn, sycamore, ash and hazel hedge, forming a 2.5m high screen. No evidence of recent breakout or significant dieback.

Tree Quality Assessment: Ref.BS5837 (2012) 4.5.1 **Category B2:** 'Trees present in numbers, usually growing as groups or woodlands, such that they collect a higher collective rating'.

Water Demand NHBC 4.2-B: High

Root Protection Area RPA: for average tree of 10cm diameter at narrowest point below fork $(0.15 \times 12) = 1.8\text{m}$ radius.

Total RPA required at current growth stage = 10.2m^2

Arboricultural Impact Assessment AIA:

- The proposed access road falls outside the RPA of H1
- No trench excavation permitted within the RPA

Method Statement: construction of new access

- Install the section of Heras fence barrier positioned as indicated on the tree protection plan. Specification as recommended in BS5837 (2012) fig.3 appended.

General Arboricultural Method Statement ref. BS 5837 (2012)

3.0 The root protection area (RPA) recommendation in BS 5837 2012 (Trees in relation to design, demolition and construction – Recommendations), is based upon a minimum area (in m^2) calculated from the measurement of the stem diameter and a factor of the radial distance between the tree stem and the outer extent of the main lateral roots. The resulting area is usually recorded as a generalised circle on the tree survey. However the significant figure is the equivalent available rooting area in m^2 rather than the circular shape; tree roots exploit the optimum ground conditions for their physical development dependant upon soil aeration, plant-available water, mineral elements and physical barriers to growth. Providing the total minimum area in m^2 recommended in the RPA is available to the tree, the actual shape of the area is less significant, *providing* it can be demonstrated that the construction process will not result in significant damage to existing roots greater than 25mm in diameter. 'The viable retention of trees on construction sites is dictated by the successful protection of their root systems throughout the development process from initial site clearance to installation of the new landscape. Healthy soils contain five basic components: oxygen, organic matter, mineral matter, living organisms and moisture. A soil's porosity allows water to drain through, carbon dioxide to escape and oxygen to enter. Construction vehicles operating on exposed soils, particularly in wet conditions, compact the soil pores and prevent these processes from occurring'(Cowan 2005)

3.1 The Tree Protection Plan (TPP) and method statement details how the construction work will be carried out in proximity to the retained trees, protective barrier specification, timing of work, other mitigation measures where required and supervision of the protection measures during construction.

3.2 Summary of works

Drainage and Utilities: Follow recommendation in the NJUG Volume 4 Code of practice relating to work in proximity to tree roots within the RPA; specifically, the avoidance of trench excavations within the RPA. Any drainage or service related works to be carried out within the Root Protection Area must be subject to the prior written approval of the LPA of a method statement detailing how such works are to be carried out and monitored, so as to avoid undue damage to the tree.

Site Compound, construction materials, soil/demolition debris storage mixing of concrete and washings: Must be located outside of the Root Protection Areas. Vehicle movements, storage of vehicles or heavy machinery, lighting of fires and no excavations or alterations of ground level is permitted within the protective barrier or areas of temporary ground protection

Method of work for individual trees retained in proximity to construction works or access to the works: refer to the work method described for each retained tree ref. section 2.2 of the report.

3.3 Protective Fencing

- Protective barriers should be erected with verticals positioned to avoid the lateral roots of the larger trees. Refer to BS 5837 (2012) figure 3 Protective barrier for details of the recommended specification.
- Protective barrier should be erected and then approved by the Local Planning Authority before the start of demolition and construction works on site, including the installation of temporary site office, storage and welfare facilities if required
- The barrier and ground protection shall be maintained in a satisfactory condition throughout the duration of development. There is to be no access or operations of any kind within the barrier, nor repositioning of the barrier even temporarily, without the prior written approval of the LPA.

Appendix 1

Photo Detail: Tree condition illustration ref. Sect 2.2






T2




T3

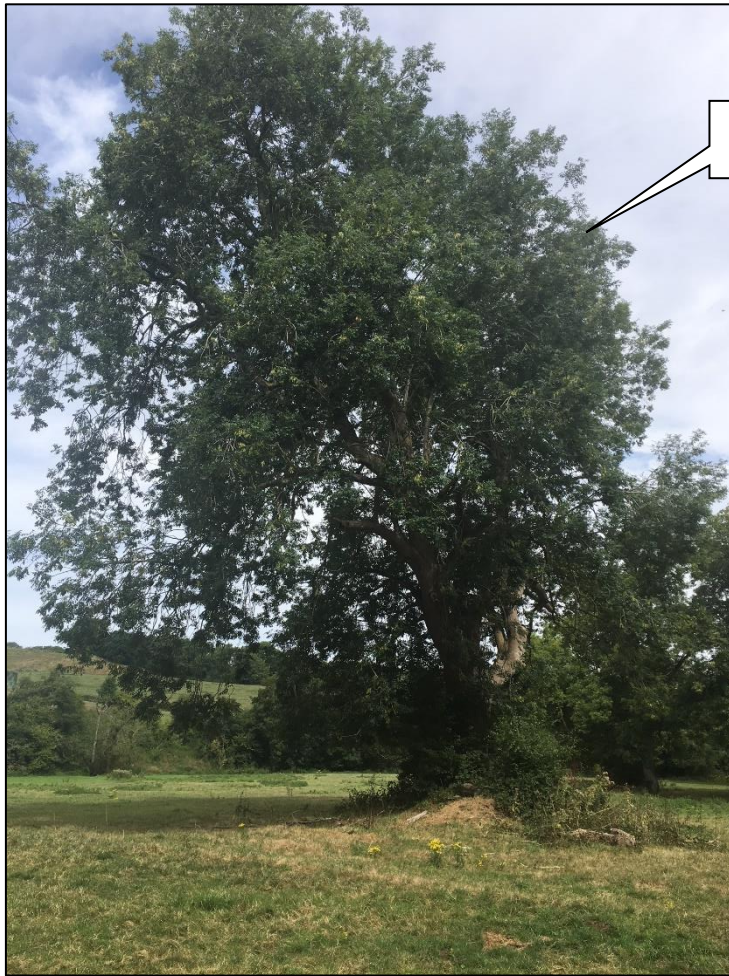

Tree Protection Plan- Forge Farm, Pont-y-Blew

06.08.2018

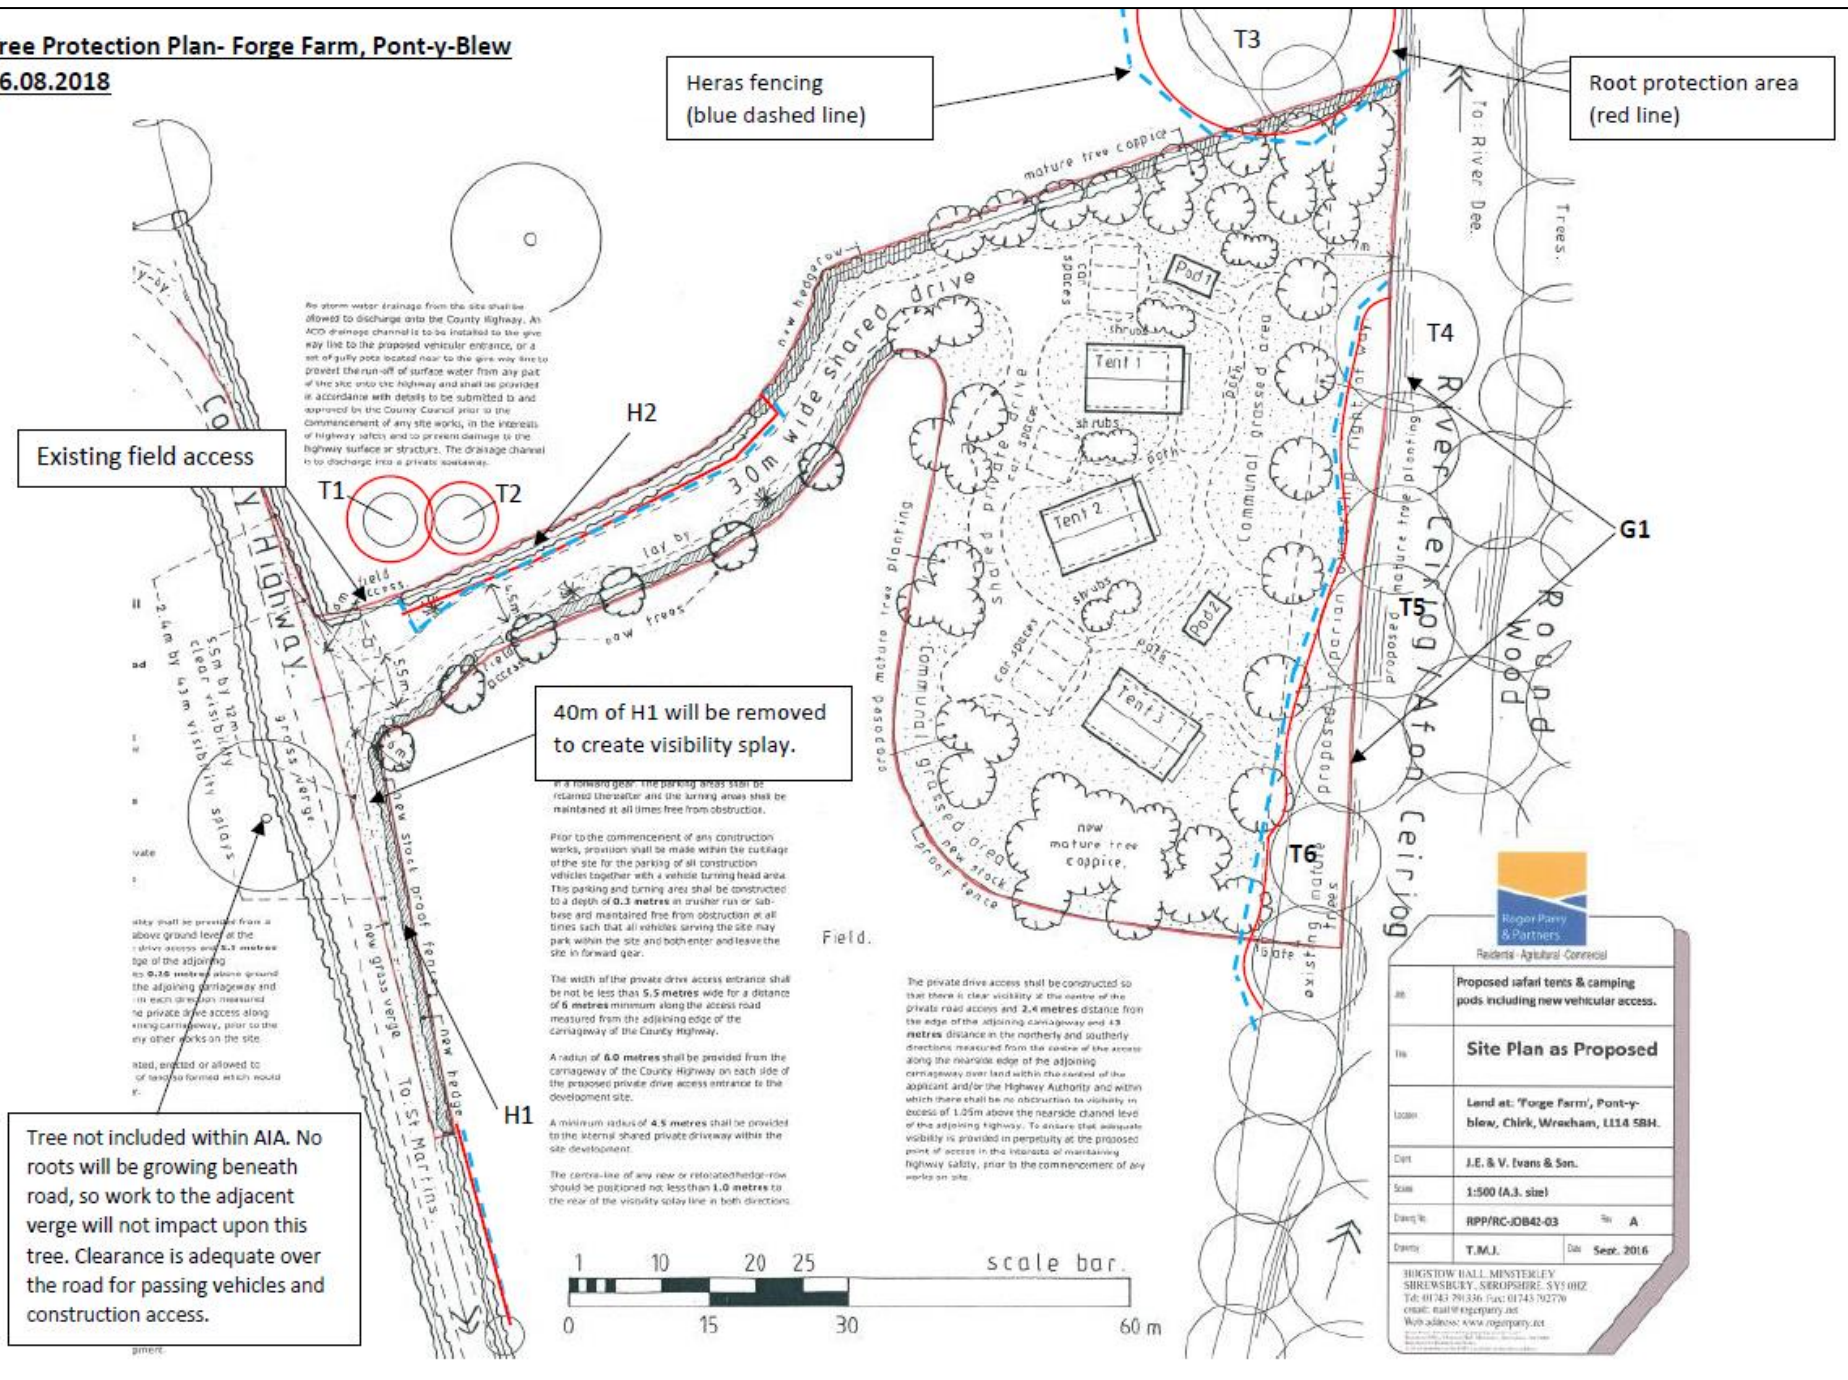


Appendix 3:


BRITISH STANDARD

BS 5837:2012

Figure 3 Examples of above-ground stabilizing systems

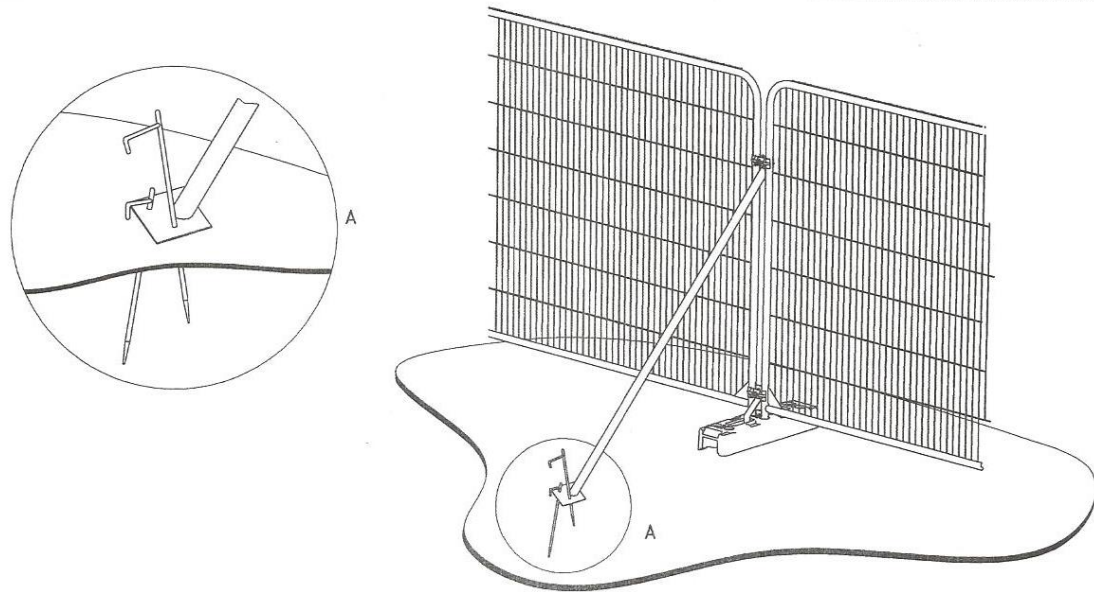

a) Stabilizer strut with base plate secured with ground pins

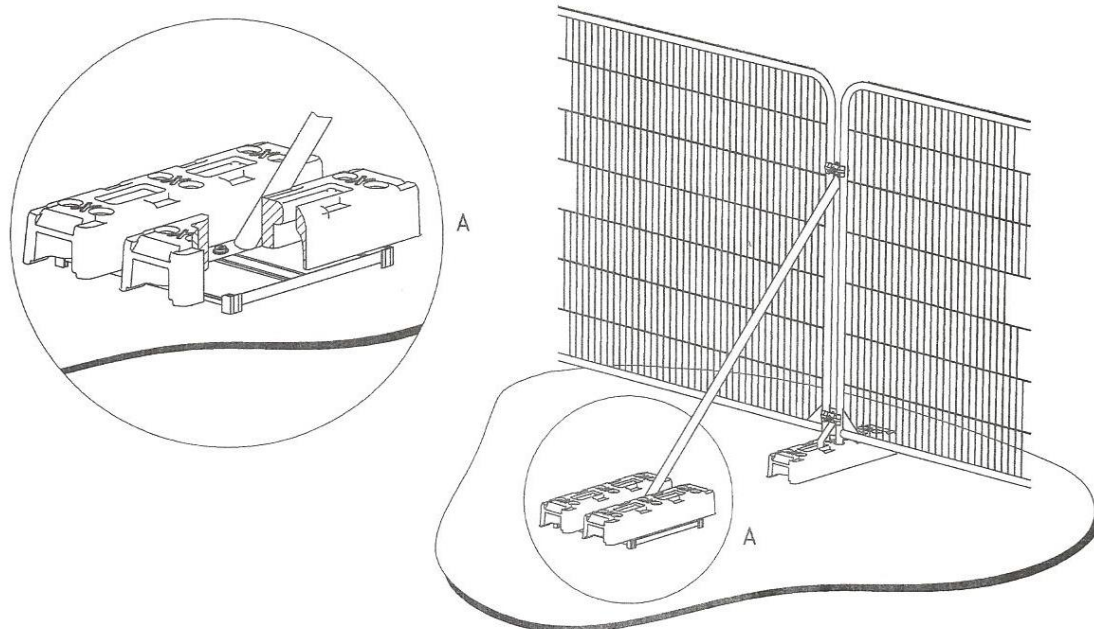

b) Stabilizer strut mounted on block tray

6.2.3 Ground protection during demolition and construction

6.2.3.2 Where the set-back of the tree protection barrier would expose unmade ground to construction damage, new temporary ground protection should be installed as part of the implementation of physical tree protection measures prior to work starting on site.

6.2.3.3 New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

NOTE The ground protection might comprise one of the following:

- a) *for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile membrane;*
- b) *for pedestrian-operated plant up to a gross weight of 2 t, proprietary, inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150 mm depth of woodchip), laid onto a geotextile membrane;*
- c) *for wheeled or tracked construction traffic exceeding 2 t gross weight, an alternative system (e.g. proprietary systems or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected.*

6.2.3.4 The locations of and design for temporary ground protection should be shown on the tree protection plan and detailed within the arboricultural method statement (see 6.1).

6.2.3.5 In all cases, the objective should be to avoid compaction of the soil, which can arise from the single passage of a heavy vehicle, especially in wet conditions, so that tree root functions remain unimpaired.

6.2.4 Additional precautions outside the exclusion zone

6.2.4.1 Planning of site operations should take sufficient account of wide loads, tall loads and plant with booms, jibs and counterweights (including drilling rigs), in order that they can operate without coming into contact with retained trees. Such contact can result in serious damage to the trees and might make their safe retention impossible. Consequently, any transit or traverse of plant in proximity to trees should be conducted under the supervision of a banksman, to ensure that adequate clearance from trees is maintained at all times. Access facilitation pruning should be undertaken where necessary to maintain this clearance.

NOTE In some instances, local planning authority consent for pruning might be required.

6.2.4.2 Fires on sites should be avoided if possible. Where they are unavoidable, they should not be lit in a position where heat could affect foliage or branches. The potential size of a fire and the wind direction should be taken into account when determining its location, and it should be attended at all times until safe enough to leave.

NOTE Local environmental health authorities might have specific restrictions.

6.2.4.3 Any materials whose accidental spillage would cause damage to a tree should be stored and handled well away from the outer edge of its RPA.

Glossary of Arboricultural Terms

Adaptive Growth: Woundwood.	New strengthening woody growth in response to loss of tissue through decay or physical damage
Age Class: Young	Up to 1/3 rd life expectancy
Early-mature	Between 1/3 rd and 2/3 rd s life expectancy
Mature	Over 2/3 rd s life expectancy
Late-mature	Onset of natural limb loss; increase in dysfunctional tissue
Over-mature	Declining or moribund trees of low vigour. NB Late-mature and over-mature trees are more prone to structural failure than young or early-mature trees.
Breakout:	Loss of a limb usually close to the junction the main stem or scaffold limb
Branch bark ridge:	Natural feature in the axil of the branch providing a simple guide for locating the best position for the top edge of a pruning cut.
Buttressing:	Root flare at the base of the stem
Crown dieback:	Significant loss of foliage throughout the crown; often the result of root damage. Usually indicating a tree in decline.
Deadwood:	Dead secondary branching persisting on the scaffold limbs. Minor deadwood <50mm diameter is less likely to cause damage in the event of failure. Major deadwood >50mm present a greater hazard and is a greater risk of failure in trees without durable heartwood e.g. Lime and ash. Deadwood which is not presenting a hazard to the highway is excluded from the inspection report. Deadwood stubs: Prevent the sealing of the wound site, providing sites of decay and increasing risk of limb failure.
Epicormic Response:	Growth of dormant buds on areas of the stem or scaffold limbs effected by loss of woody tissue or foliage. New woody tissue is laid down in areas of vigorous epicormic growth.
Included bark:	Weak regions of bark-to-bark contact at the stem or branch junctions.
Retrenchment:	Describes the response in new growth in the lower crown, following dieback in the upper crown. A feature of some over-mature trees, enabling survival into great age (veteran trees)
Scaffold limbs:	1 st order limbs; the major limbs supporting the secondary branching or 2 nd & 3 rd order branches
Soil Heave:	Raised lateral roots or loosened soil surrounding the base of the tree.

Willowmead Publishing Ltd

Opik H & Rolfe S (2005) *The Physiology of Flowering Plants* Cambridge

Lonsdale D, (1999) *Principles of Tree Hazard Assessment and Management* HMSO

Mattheck & Breloer (1994) *The body language of trees* DTR TSO

Mattheck C, (2007) Updated Field Guide for Visual Tree Assessment

Forschungszentrum Karlsruhe GmbH

Roberts J, Jackson N, Smith M (2006) *Tree Roots in the Built Environment* TSO

Strouts & Winter, (1994) *Diagnosis of ill-health in trees* D.o.E HMSO

Weber & Mattheck (2001) *Manual of Wood Decays in Trees* Arboricultural Association

White, White & Walters (2005) *Trees; A field Guide to the trees of Britain and Northern Europe*. Oxford

Arb Implication Assessment: Zoe Adlington BSc, MArborA

Date: 06.08.2018
