


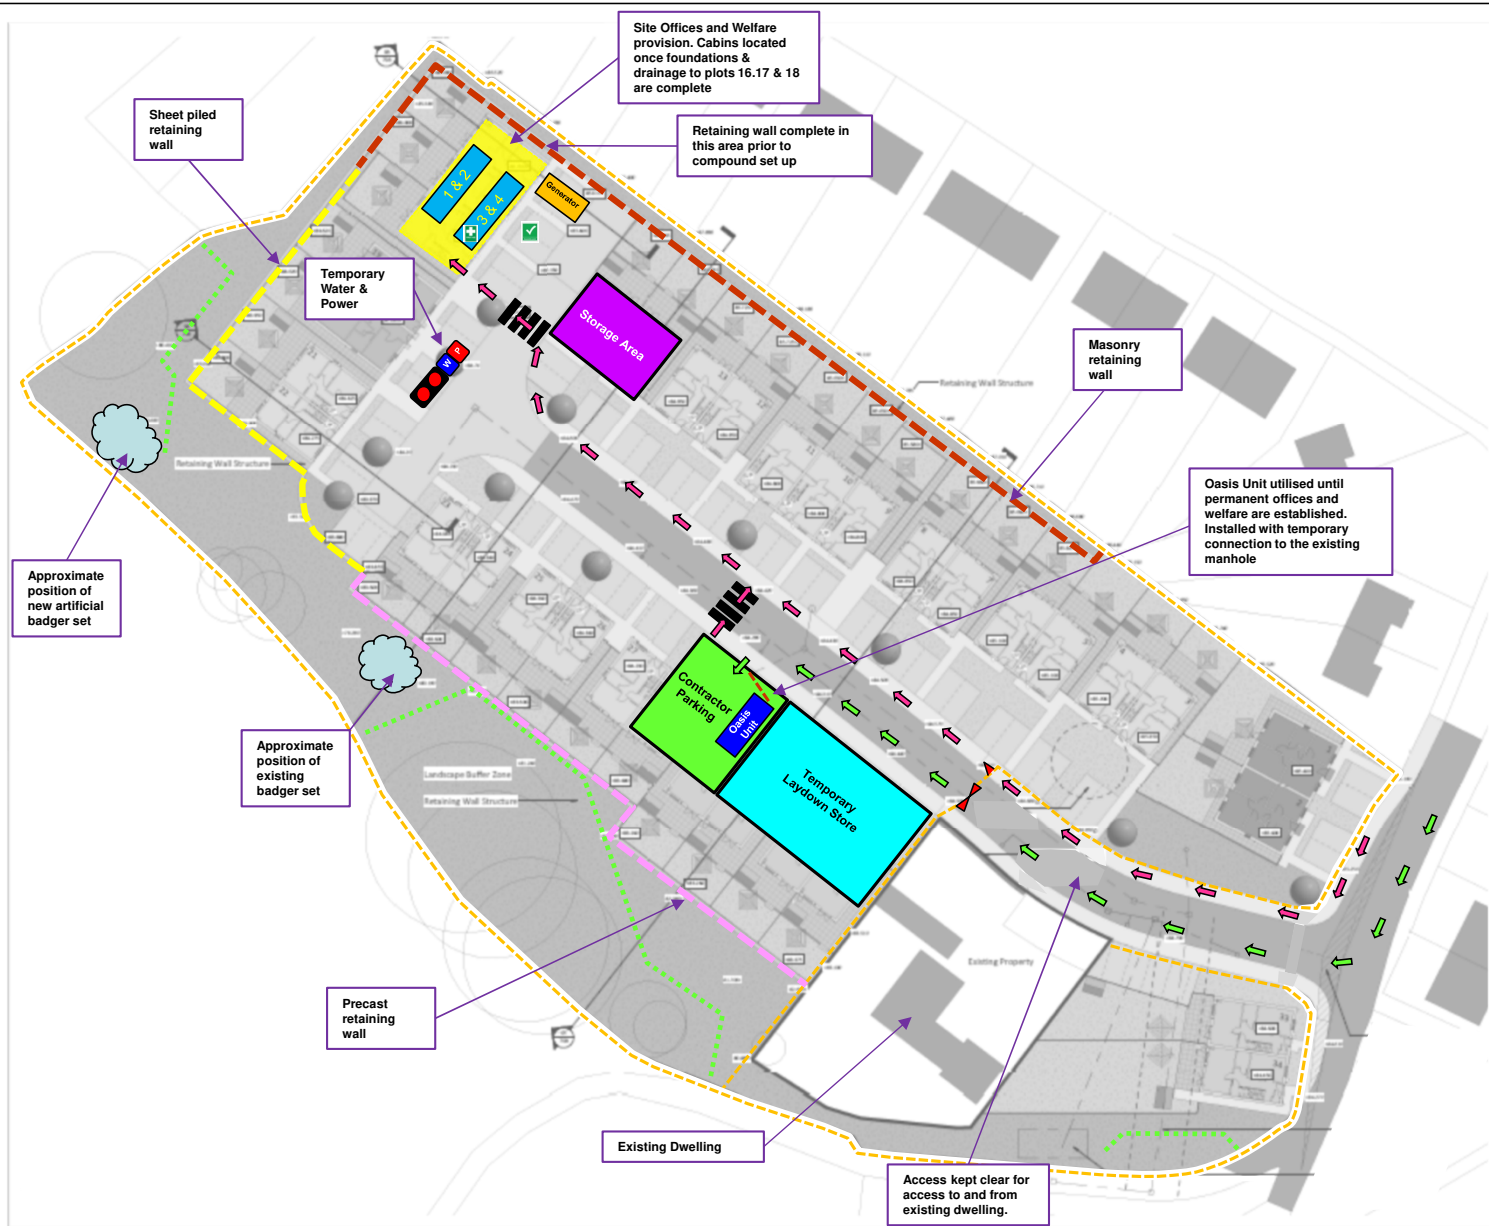

Key

Site Cabins & Welfare (32ft units stacked)

1 & 2 Toilets (bottom) / Meeting room (top)
3 & 4 Canteen (bottom) / Office (top)

Temporary Water & Power

Vehicular access

Pedestrian access

Site fencing / boundary fencing

Tree Protection Fencing

Storage Area

Temporary Storage Area

First Aid Area

Fire Muster Point

Mortar Silos

Vehicle access gate

Pedestrian Access Gate

Pedestrian Crossing Point

Notes:

- A separate vehicle access gate and pedestrian gate will be provided at the entrance to the site.
- Operative and vehicular access will be segregated using pedestrian barriers and walkways.
- The entrance to the existing property, located on site, will remain clear and unobstructive at all times.
- Pedestrian crossing points will be located on site to allow safe access for operatives crossing within the site.
- Site Welfare will consist of Canteen/ drying room, male and female toilets with associated power, lighting and water.
- The site will be damped down to prevent the impact of dust migration to the surrounding properties.
- All skip vehicles leaving site will be covered.
- Vehicles will turn around within the confines of the site. No vehicles will be allowed to reverse onto Heol Berwyn.
- No vehicles will be allowed to wait on Heol Berwyn. A vehicle waiting zone will be provided within the confines of the site.
- All road surfaces are to be kept clean at all times with periodic road cleaning.
- Vehicles will be administered by a fully trained banksman.
- Limited parking will be available on site during the course of the construction works.
- We will encourage car sharing to minimise the parking requirements in and around site.
- Working hours will be 8.00am to 5.00pm Monday to Friday
- Programme for the construction works is 65 weeks.



Wales & West Housing
Wrenbury Way
34 Dwelling Development

Site Logistics & Traffic Management Plan

Date: 08/04/21

Revision : 30/04/21

Revision Date: A

