

ARBORICULTURAL METHOD STATEMENT **STABLES – TREWYTHEN HALL RESIDENTIAL CARE HOME**

SEQUENCE OF OPERATIONS

From commencement of the above development, the following methodology shall be implemented in the manner and sequence described:

1. Tree surgery works
2. Erect temporary protective fencing
3. Main construction phase
4. Removal of temporary fencing
5. Landscaping within RPA's
6. Arboricultural site supervision

1. Tree Surgery Works

1. Before the erection of the temporary protective fencing, all tree surgery works shall be implemented in accordance with the Tree Survey Schedule at **Appendix 1**
2. All possible efforts must be made to prevent damage to retained trees including potential root incursion or compaction caused by vehicle access.
3. All arboricultural works shall conform to the recommendations of BS 3998 (2010) 'Recommendations for Tree Work'
4. All operatives shall be equipped with and use personal protective equipment (PPE) in accordance with current Health & Safety Executive current directives and industry codes of practice.
5. Performance of all arboricultural operations and use of equipment shall be in accordance with current Health & Safety Executive current directives and industry codes of practice

2. Erect Temporary Tree Protective Fencing

1. Prior to commencement of any construction, preparation, excavation or material deliveries the main contractor shall erect the temporary protective fencing as detailed in the 'Tree Protection Specification' and in the location indicated on the Tree Protection Plan.

3. Main Construction Phase

1. There shall be no storage of construction material, site parking, site accommodation or equipment in any area designated as the Root Protection Area (RPA) and Construction Exclusion Zone (CEZ) and enclosed by Temporary Protective Fencing
2. No materials that are likely to have an adverse effect on tree health such as oil, bitumen or cement will be stored or discharged within 10 metres of the trunk of a tree that is to be retained. No fires will be lit
3. The site agent shall supervise deliveries by self-loading crane, with vehicles positioned in such a manner that retained trees are not at risk of damage

Cement Mixing

- The cement mixer will be laid on top of plywood boards in a position outside the RPA of any trees. The mixer will be kept in this position throughout all development work.

Avoiding Damage to Stems and Branches

- Care shall be taken when planning site operations in proximity to trees to ensure that wide or tall loads or plant with booms, jibs and counterweights can operate without encountering retained trees. Such contact can result in serious injury resulting in safe retention impossible

On Site Storage of Spoil and Building Materials

- Prior to and during all site construction works no spoil will be stored and no cement mixing will take place within the Root Protection Area of any tree on or adjacent to the site even if proposed site work is to be within the crown spread. Any encroachment within this protected area will only be with the prior agreement of the LPA Arboricultural Officer

4. Remove all Temporary Tree Protective Fencing

1. Tree Protective fencing will only be removed upon completion of all construction work and once all machinery associated with the works has left site.

5. Landscaping within RPA of Trees

1. There shall be **no rotovating** of ground within any area designated as a Root Protection Area (RPA) and Construction Exclusion Zone (CEZ) and enclosed by Temporary Protective Fencing.
2. No hard-landscaping works or excavation for cables or any other service should be installed within the Root Protection Area (RPA) and Construction Exclusion Zone (CEZ) without the written consent of the LPA

6. ARBORICULTURAL SITE SUPERVISION

- 1 The erection of all tree protection measures outlined in this AMS and as indicated on the Tree Protection Plan will be inspected by the contract Arboricultural Consultant immediately after erection. Photographic evidence of the location and specification of all protective fencing will be forwarded to the LPA Tree Officer upon completion.
- 2 Any proposed work within any designated RPA will be overseen by contract Arboricultural Consultant with photographic records taken and signed inspection report emailed direct to the LPA for approval

Contacts

Arboricultural Consultant

Name: Alistair Henderson
Tel: 01244 389114
Mobile: 07766 774508
Email: alistair@tree-solutions.co.uk

WCBC Arboricultural Officer

Name: Jon Brewin
Tel: 01978 298763
Email: jon.brewin@wrexham.gov.uk

TREE PROTECTIVE FENCING

- 1 Before the commencement of any demolition and subsequent construction works on site (other than those set out in the schedule of tree works contained in this document), protective fencing will be erected as detailed on the Tree Protection Plan and as specified below. The LPA Tree Officer will be given 5 days' notice upon completion of the fencing to inspect and approve prior to the commencement of any site works.
- 2 The fencing will consist of a scaffold framework in accordance with Figure 2 of BS 5837 – 2012 (illustration below) comprising a metal framework, both vertical and horizontal, well braced to resist impacts. Vertical tubes will be spaced at a maximum interval of 3m. Onto this, weldmesh panels shall be securely fixed with wire or scaffold clamps. Weldmesh panels on rubber or concrete feet are not considered resistant to impact and for this reason will not be used. The site manager or other suitably qualified appointed person will be responsible for inspecting the protective fencing on a daily basis; any damage to the fencing or breaches of the fenced area will be rectified immediately.
- 3 Clearly legible weatherproof signage, stating "Protected Trees – Exclusion Zone" shall be attached to the fencing 1.5m from the ground, facing out of the Tree Protection Zone located at regular intervals along the fence line
- 4 The fencing will remain in place until completion of all site works and then only removed when all site traffic is removed from site
- 5 Other than works detailed within this method statement or approved in writing by the Local Planning Authority (LPA), no works including storage or dumping of materials shall take place within the exclusion zones defined by the protective fencing.

Protective Fencing Detail

1. **Magenta** - Trees



Tree Protective Fencing Specification

Appendix One
Tree Survey Schedule

TREE SURVEY SCHEDULE (BS5837: 2012)

Tree Solutions

Arboricultural Consultants

SITE:	LAND AT TREWYTHEN HALL, GRESFORD
CLIENT:	TREWYTHEN HALL RESIDENTIAL CARE HOME
BRIEF:	ARBORICULTURAL METHOD STATEMENT - STABLES

SURVEYOR:	A. HENDERSON
ASSESSMENT DATE:	20/06/2020
VIEWING CONDITIONS:	GOOD
JOB REFERENCE:	20/AMS/WXM/260

PAGE 1 OF 3

TREE NO. T - Tree G - Group H - Hedge	SPECIES (COMMON NAME)	AGE	HEIGHT (m) + CROWN CLEARANCE/ DIRECTION OF GROWTH (N.S.E.W)	RADIAL CROWN SPREAD (m)				STEM/ MULTI-STEM* DIA. (mm)	VITALITY	COMMENTS	MANAGEMENT	CATEGORY & SUB-CATEGORY GRADING BS 5837	BS 5837 RADIUS (m) RPA (m²)
				N	S	E	W						
T21	Yew (Irish)	M	10 0	2.5	2.5	2.5	2.5	600	G	- Good quality specimen tree - E.R.C. 40	• N/A	A1	7 163m²
T22	Cedar (Lebanon)	FM	18 0.5N	9	10	8.5	8	980	G	- Good quality specimen tree - E.R.C. 40	• N/A	A1	12 435m²
T23	Beech	FM	18 0.5W	8	11	5	7	825	M	2 stems from base (640 & 520mm – diameter combined as per BS) - Large wide spreading tree with acute union between stems at base and fused main leaders in crown - Would open vista to T22 if removed - E.R.C. 20	• No works	B2	10 308m²
T24	Beech	EM	16 5W	4	2	2	3	380	M	- Overgrown self-set tree with no particular value - Would open vista to T22 if removed - E.R.C. 10	• No works	C2	4.5 65m²

HEADINGS & ABBREVIATIONS

TREE NO.
SPECIES:
AGE RANGE/LIFE STAGE:
HEIGHT:
CROWN SPREAD:
CROWN CLEARANCE & DIRECTION OF GROWTH:
STEM DIA/MULTI-STEM DIA:
VITALITY:
E.R.C. = ESTIMATED REMAINING CONTRIBUTION:
BS 5837 CATEGORY & SUB-CATEGORY GRADING:
BS 5837 RADIUS & BS 5837 RPA:

REFERENCE NUMBER. REFER TO PLAN OR NUMBERED TAGS WHERE APPLICABLE (T = TREE, G = GROUP, H = HEDGE)
COMMON NAME (LATIN NAMES AVAILABLE ON REQUEST)
Y = YOUNG, SM = SEMI MATURE, EM = EARLY MATURE, M = MATURE, PM = POST MATURE
ESTIMATED AND RECORDED IN METRES. APPROXIMATELY 1 IN 10 TREES ARE MEASURED USING A CLINOMETER AND THE REMAINDER ESTIMATED AGAINST THE MEASURED TREES
MAXIMUM CROWN RADIUS MEASURED TO THE FOUR CARDINAL COMPASS POINTS FOR SINGLE SPECIMENS ONLY (MEASUREMENT FOR TREE GROUPS - MAXIMUM RADIUS OF THE GROUP)
HEIGHT IN METERS OF CROWN CLEARANCE ABOVE ADJACENT GROUND LEVEL (TO INFORM ON GROUND CLEARANCE, CROWN/STEM RATIO AND SHADING)
STEM DIAMETER - MEASURED AT APPROXIMATELY 1.5 METRES ABOVE GROUND LEVEL OR A COMBINATION OF STEMS FOR MULTI-STEMMED TREES
A MEASURE OF PHYSIOLOGICAL CONDITION. D = DEAD, MD = MORIBUND, P = POOR, M = MODERATE, G = GOOD
RELATIVE USEFUL LIFE EXPECTANCY (YEARS)
A = HIGH QUALITY AND VALUE, B = MODERATE QUALITY AND VALUE, C = LOW QUALITY AND VALUE, U = UNSUITABLE FOR RETENTION (SUB-CATEGORY REFERS TO ARBORICULTURAL, LANDSCAPE AND CULTURAL/CONSERVATION VALUES)
PROTECTIVE DISTANCE - RADIUS FROM THE CENTRE OF THE STEM TO THE LINE OF TREE PROTECTION (CONSTRUCTION EXCLUSION ZONE - CEZ) AND PROTECTIVE BARRIER ROOT PROTECTION AREA - BS 5837 (2012) ANNEX D (THE RECOMMENDATIONS STATE THAT THE RPA SHOULD BE CAPPED AT 707 M²) NOTE – ALL CALCULATIONS ROUNDED TO NEAREST DECIMAL

TREE SURVEY SCHEDULE (BS5837: 2012)

Tree Solutions

Arboricultural Consultants

SITE:	LAND AT TREWYTHEN HALL, GRESFORD
CLIENT:	TREWYTHEN HALL RESIDENTIAL CARE HOME
BRIEF:	ARBORICULTURAL METHOD STATEMENT - STABLES

SURVEYOR:	A. HENDERSON
ASSESSMENT DATE:	20/06/2020
VIEWING CONDITIONS:	GOOD
JOB REFERENCE:	20/AMS/WXM/260

PAGE 2 OF 3

TREE NO. T - Tree G - Group H - Hedge	SPECIES (COMMON NAME)	AGE	HEIGHT (m) + CROWN CLEARANCE/ DIRECTION OF GROWTH (N.S.E.W)	RADIAL CROWN SPREAD (m)				STEM/ MULTI-STEM DIA. (mm)	VITALITY	COMMENTS	MANAGEMENT	CATEGORY & SUB-CATEGORY GRADING BS 5837	BS 5837 RADIUS (m) RPA (m²)
				N	S	E	W						
T25	Sycamore	M	16 1S	3	5	4	5	630	M	- Ivy clad insignificant overgrown self-set tree due to lack of past management - Would open vista to T22 if removed - E.R.C. 20	• As T23	C2	7.5 180m²
T26	Pine	M	12 0	3	4	2	2	530	M	- Part of group of 3 trees forming closed canopy - E.R.C. 20	• No works	B2	6.5 127m²
T27	Pine	M	12 1N	5	1	1	3	420	M	• As T26	• No works	B2	5 80m²
TT28	Pine	M	12 4S	2	1.5	3	2	520	M	• As T26	• No works	B2	6.5 122m²
T30	Oak	FM	15 0.5W	9	10	10	9	780	G	- Good quality tree - E.R.C. 40+	• N/A	A1	9.5 275m²
T31	Monkey Puzzle	M	13 3W	2.5	2.5	2.5	2.5	540	M	- Insignificant tree - E.R.C. 20	• Consider removal if required	B2	6.5 132m²
T33	Cedar	FM	18 1N	10	11	8	11	1300	G	- Good quality specimen tree - E.R.C. 40	• N/A	A1	15 707m²

TREE SURVEY SCHEDULE (BS5837: 2012)

Tree Solutions

Arboricultural Consultants

SITE:	LAND AT TREWYTHEN HALL, GRESFORD
CLIENT:	TREWYTHEN HALL RESIDENTIAL CARE HOME
BRIEF:	ARBORICULTURAL METHOD STATEMENT - STABLES

SURVEYOR:	A. HENDERSON
ASSESSMENT DATE:	20/06/2020
VIEWING CONDITIONS:	GOOD
JOB REFERENCE:	20/AMS/WXM/260

PAGE 3 OF 3


TREE NO. T - Tree G - Group H - Hedge	SPECIES (COMMON NAME)	AGE	HEIGHT (m) + CROWN CLEARANCE/ DIRECTION OF GROWTH (N.S.E.W)	RADIAL CROWN SPREAD (m)				STEM/ MULTI-STEM* DIA. (mm)	VITALITY	COMMENTS	MANAGEMENT	CATEGORY & SUB-CATEGORY GRADING BS 5837	BS 5837 RADIUS (m) RPA (m²)
				N	S	E	W						
G4	Pine									- Poor quality trees with failed tops - E.R.C. <10	• Remove	U	N/A
G5	Pine	M	12 0	2	2.5	2	2	≤420	G	- Attractive small group worth retaining if possible - E.R.C. 20+	• N/A	B2	5 80m²

Table 1 Cascade chart for tree quality assessment

Category and definition	Criteria (including subcategories where appropriate)			Identification on plan
Trees unsuitable for retention (see Note)				
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) - Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline - Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality <i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.</i>			See Table 2
	1 Mainly arboricultural qualities	2 Mainly landscape qualities	3 Mainly cultural values, including conservation	
Trees to be considered for retention				
Category A Trees of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	See Table 2
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality	Trees with material conservation or other cultural value	See Table 2
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits	Trees with no material conservation or other cultural value	See Table 2

Appendix Two

Arboricultural Impact Plan

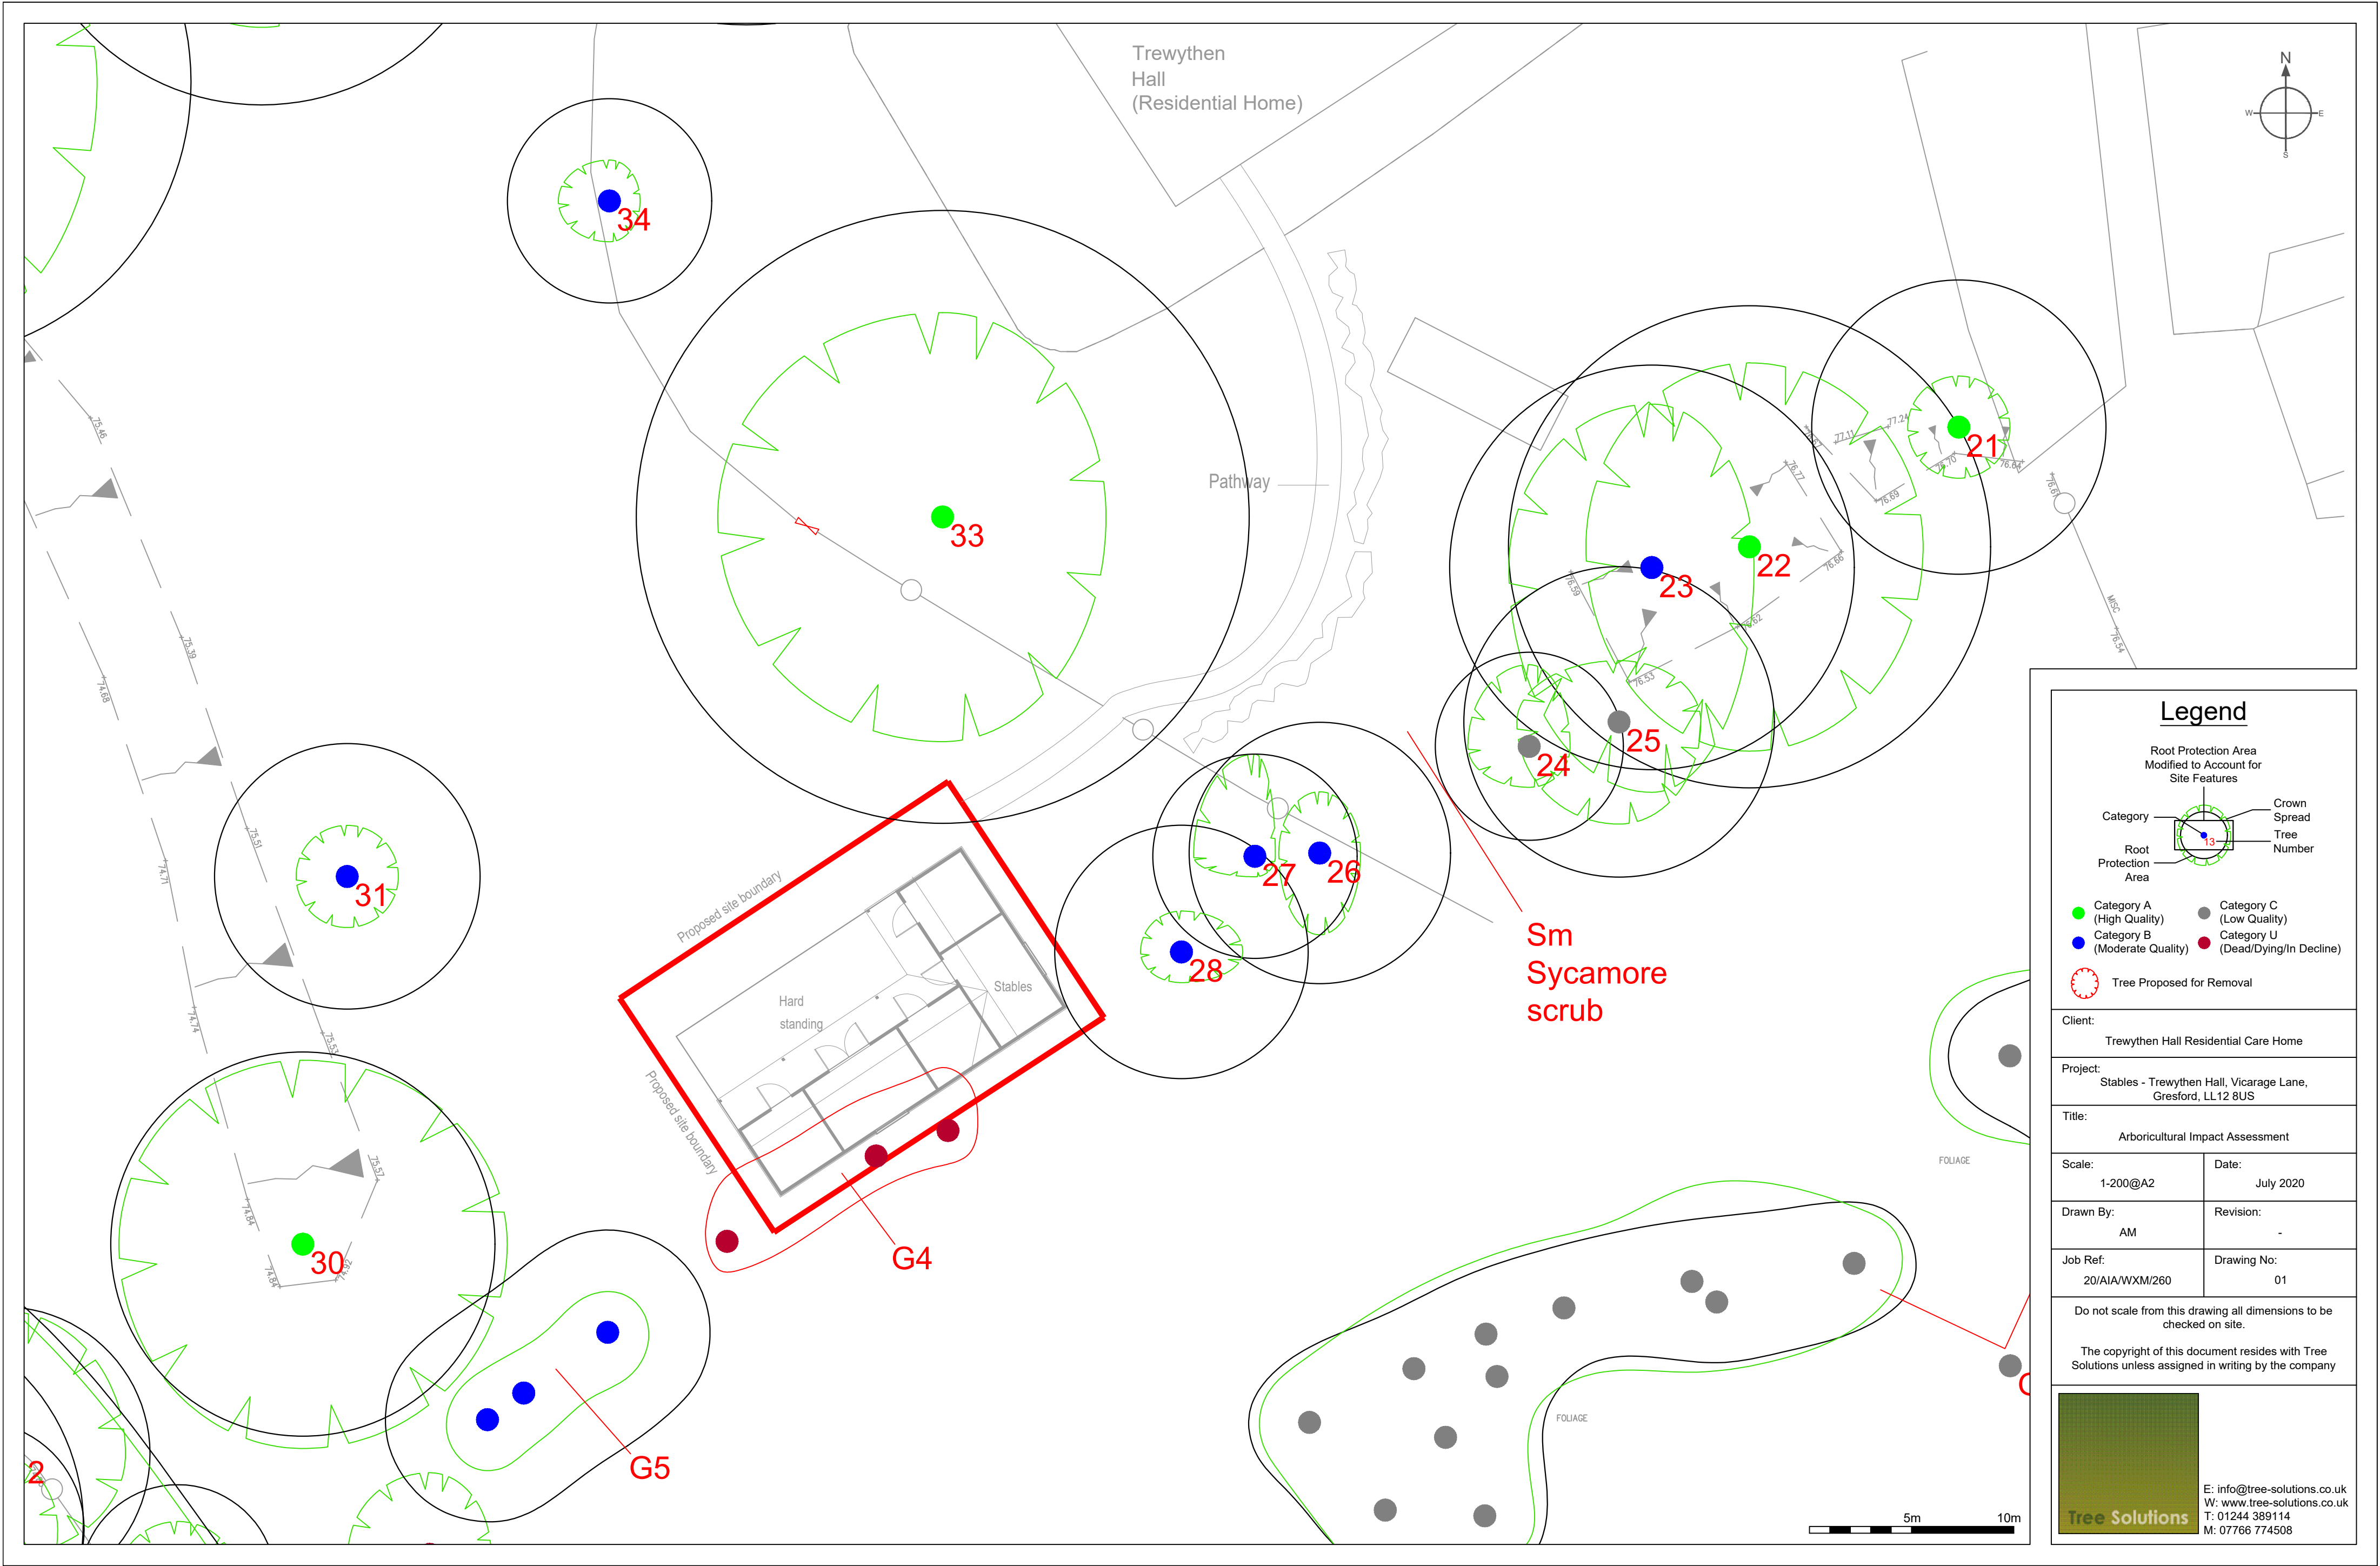

Appendix Three


Tree Protection Plan



Tree Protective Fencing Specification

PROTECTIVE FENCING. THIS FENCING MUST BE MAINTAINED IN ACCORDANCE WITH THE APPROVED PLANS AND DRAWINGS FOR THIS DEVELOPMENT.

**TREE PROTECTION AREA
KEEP OUT !**
(TOWN & COUNTRY PLANNING ACT 1990)
TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS ANTIOR ARE THE SUBJECTS OF A TREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL PROSECUTION.
ANY INCLUSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY.

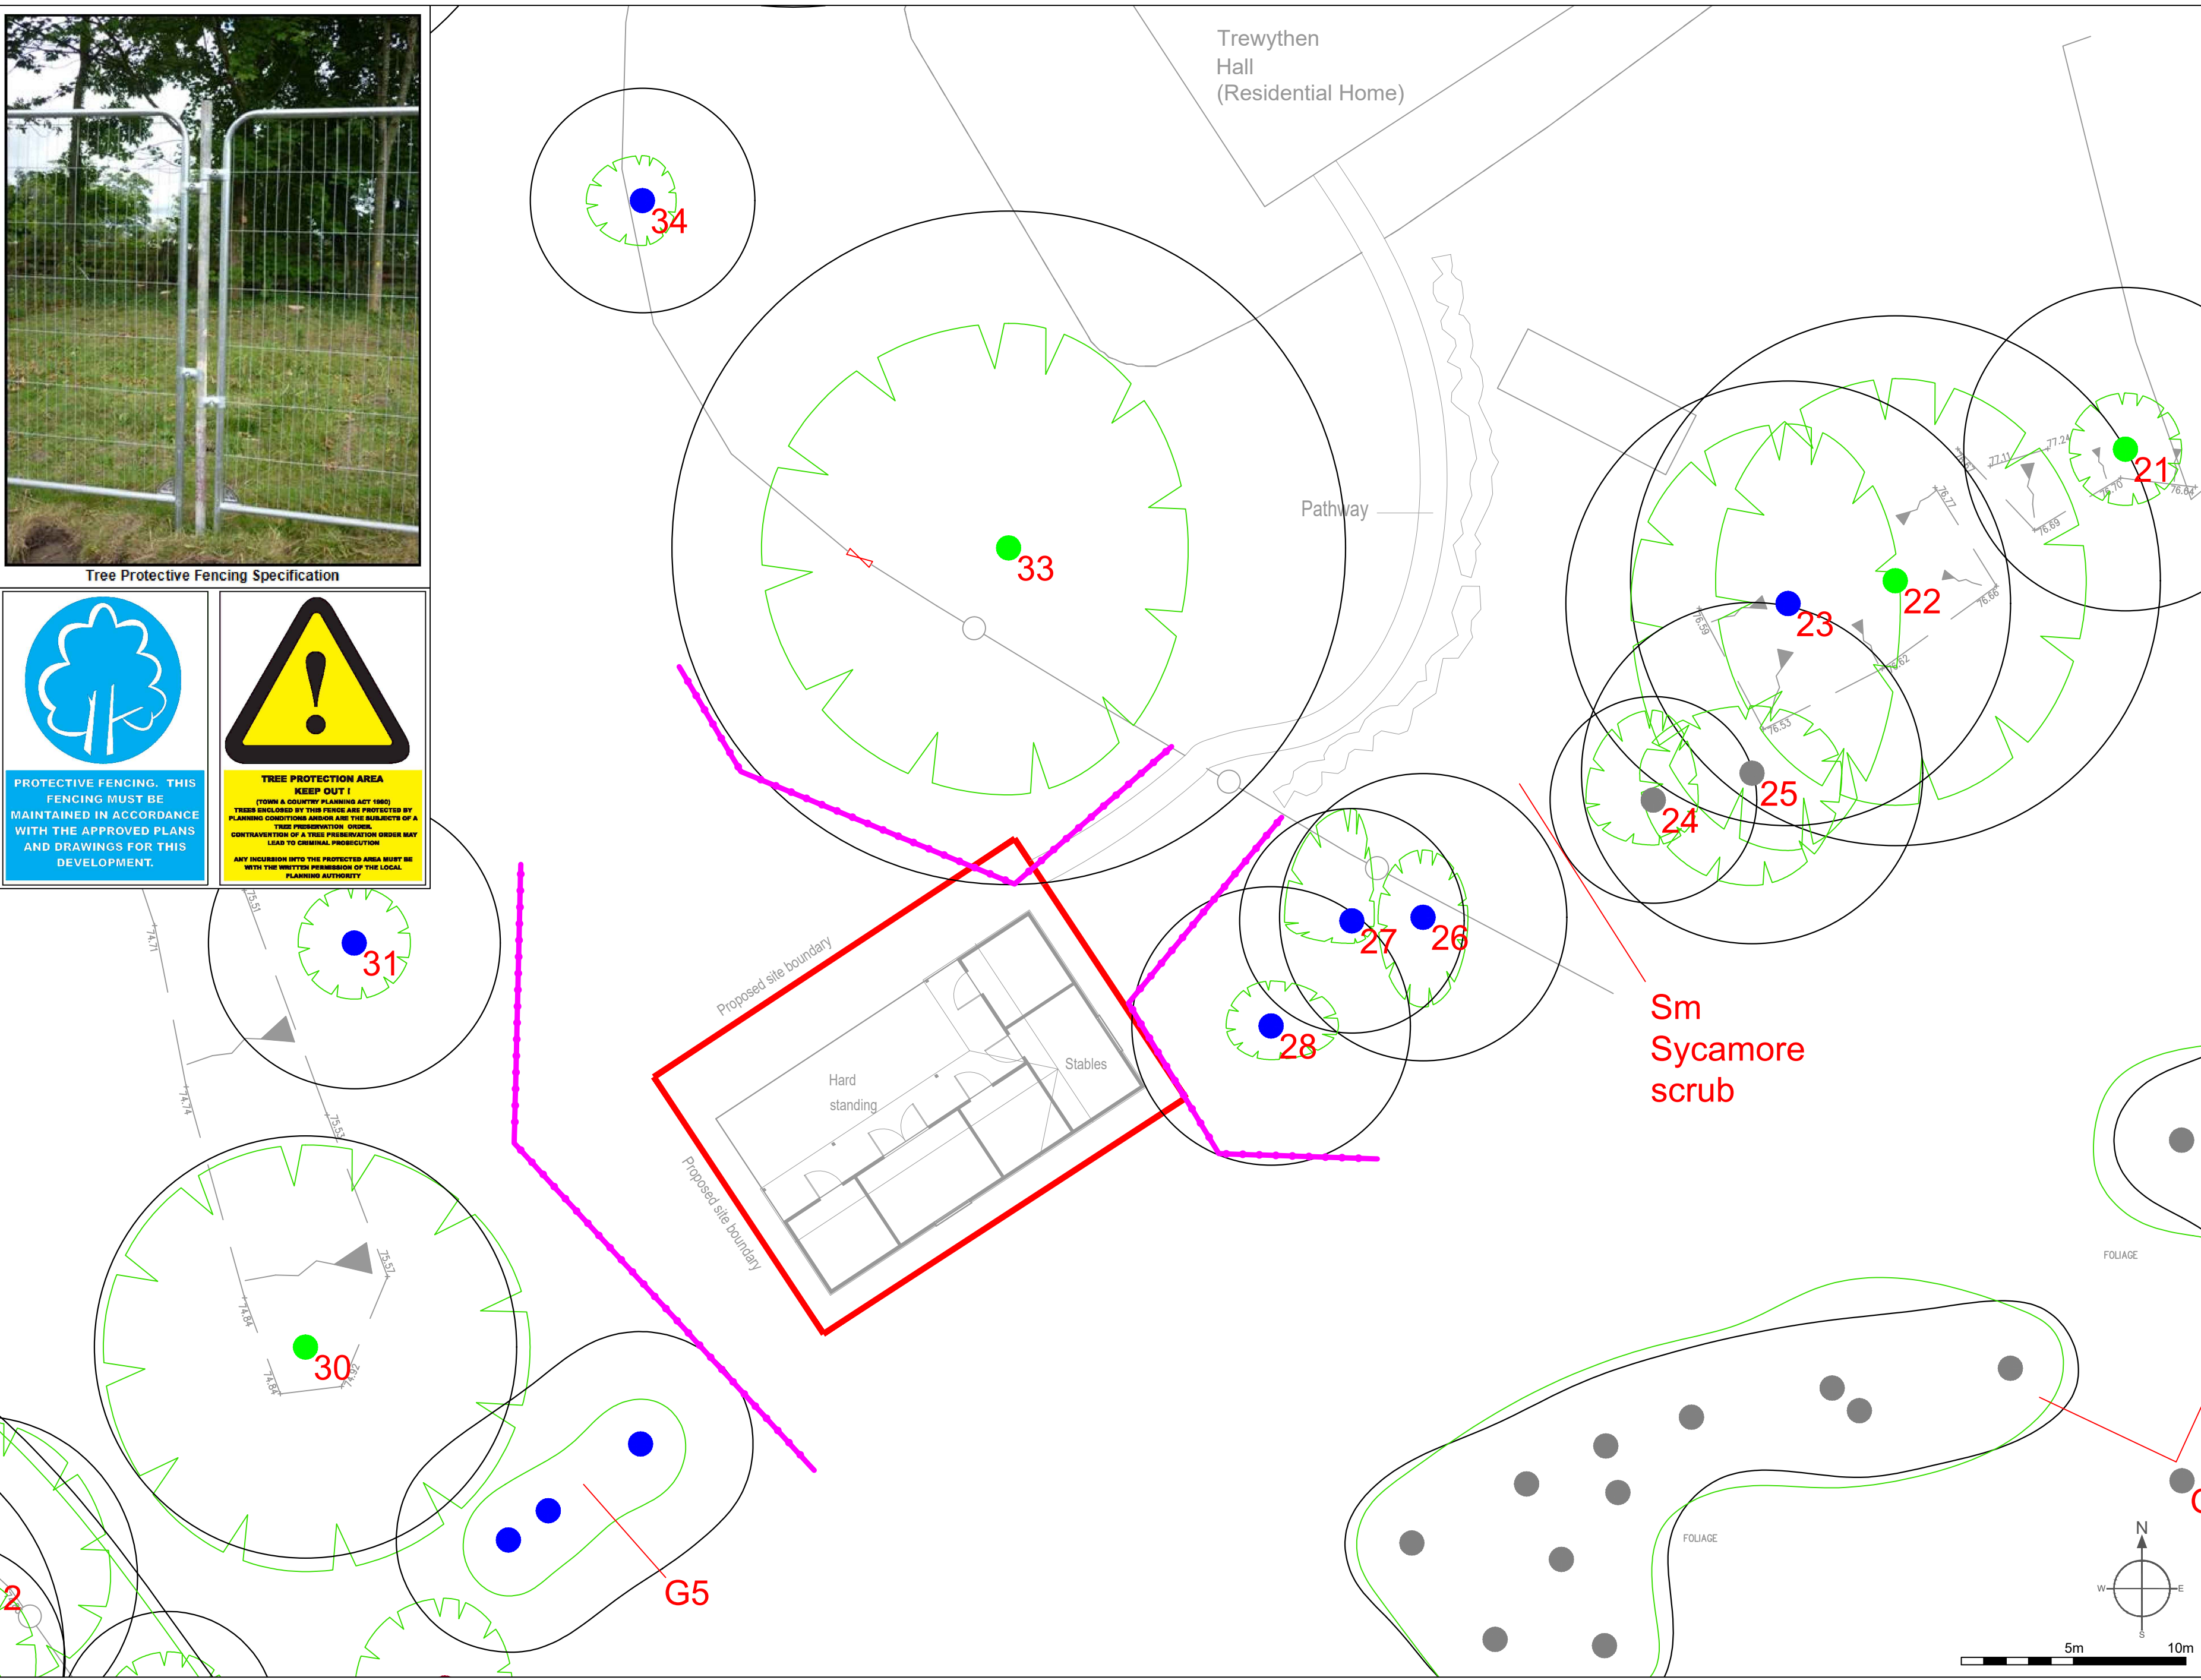

Legend

Root Protection Area Modified to Account for Site Features

Category A (High Quality) Category C (Low Quality)
Category B (Moderate Quality) Category U (Dead/Dying/In Decline)

2.0M high Heras (with extra central support bar) mounted on scaffold poles (driven in to the ground) and secured with anti tamper bolts – as illustrated.

Client: Trewythen Hall Residential Care Home	
Project: Stables - Trewythen Hall, Vicarage Lane, Gresford, LL12 8US	
Title: Tree Protection Plan	
Scale: 1-200@A2	Date: July 2020
Drawn By: AM	Revision: -
Job Ref: 20/AIA/WXM/260	Drawing No: 02

Do not scale from this drawing all dimensions to be checked on site.

The copyright of this document resides with Tree Solutions unless assigned in writing by the company

E: info@tree-solutions.co.uk
W: www.tree-solutions.co.uk
T: 01244 389114
M: 07766 774508
