Page No:

Date:

NORTH WALES PRISON

SOFT LANDSCAPING PROGRAMME (AT IPP TO DPP STAGE)(UNBUFFERED)

Lend Lease

No	Activity
	Period No
1	**Soft Landscaping Design**
2	Commencement
3	Design
4	Submit to Planners
5	
6	**Planting Seasons**
7	
8	**Landscaping adjacent to Housing**
9	Submit to Planners
10	Planning determination
11	Procure / lead-in
12	Lend Lease Community Day
13	Soft landscaping works
14	
15	**Main Works**
16	**Sectional Completion 1**
17	Car parks
18	Buildings 100, 101 & 102 External works
19	Soft landscaping works
20	
21	**Sectional Completion 2**
22	Buildings 103, 104, 105 & 107 External works
23	Soft landscaping works
24	
25	**Sectional Completion 3**
26	Buildings 106, 108A & 109 External works
27	Soft landscaping works
28	
29	**Sectional Completion 4**
30	Buildings 108B External works
31	Soft landscaping works
32	
33	**Sectional Completion 5**
34	Buildings 108C & 110 External works
35	Soft landscaping works
36	
37	**Sectional Completion 6**
38	Remaining external works outside secure zone
39	Soft landscaping works
40	
41	
42	
43	
44	
45	
46	
47	
48	
49	
50	

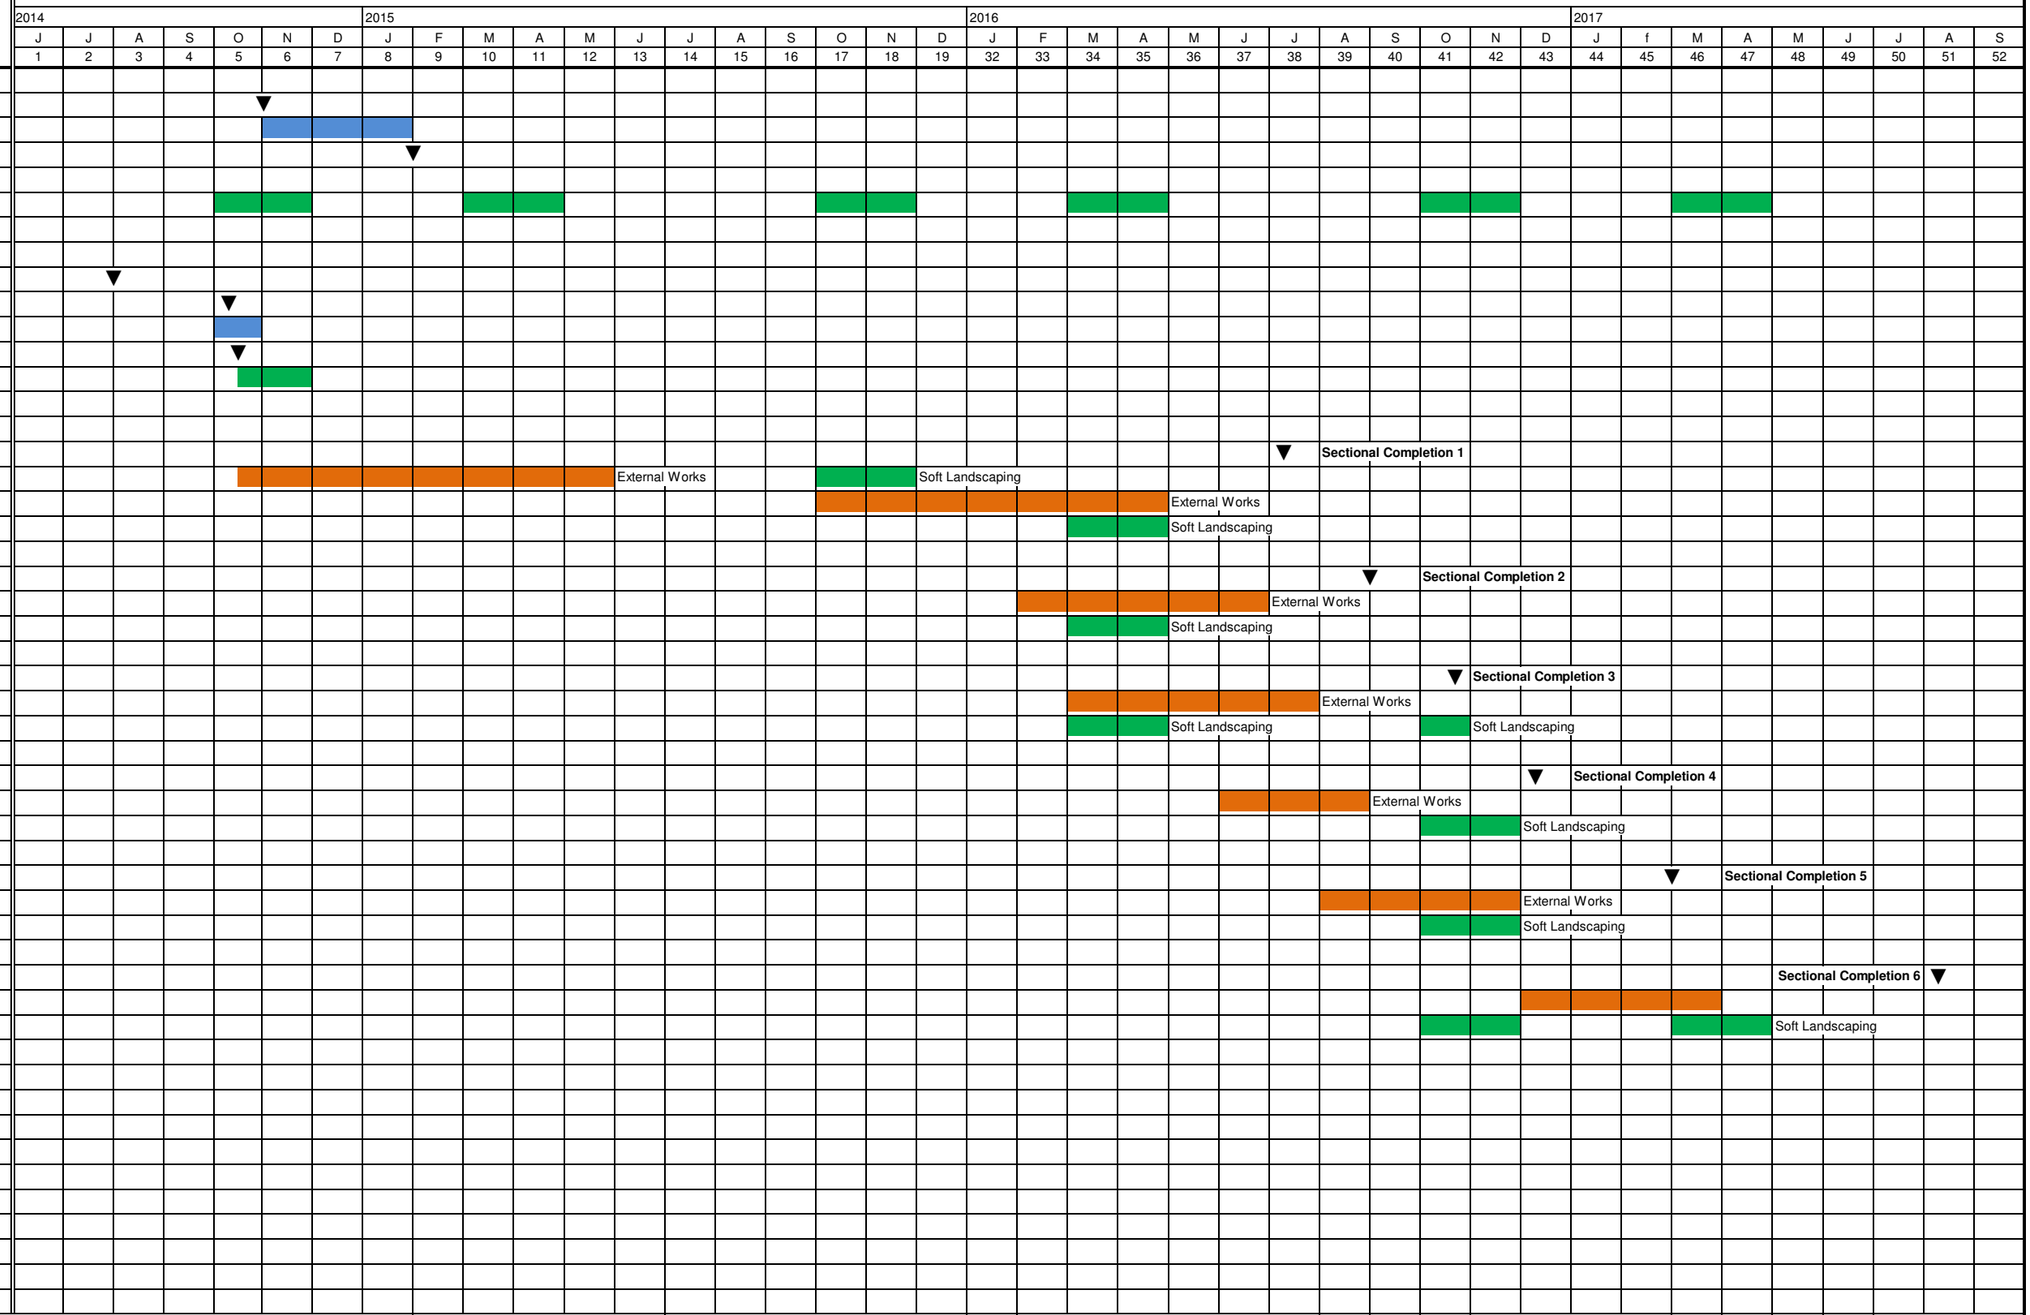

Drg No:	9500/01	Prepared by:	C Hibberd
Rev No	0	Approved by:	
Date:	25-Sep-14		
